



PARKWAY MIDDLE SCHOOL

ENTRY IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE Current scope to include monument signage, landscaping, hardscaping, marquee signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9106	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	A	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	Online Map Link			


ENTRANCE SCHEMATIC




PROJECT FINANCIALS

PROGRAM FUND	136,235,372	PROJECT COMMITMENTS	118,524	COST TO DATE	22,215
PROJECT BUDGET	628,359	% COMMITMENTED	18.86%	REMAINING BUDGET	606,144

BUDGET COMPOSITION

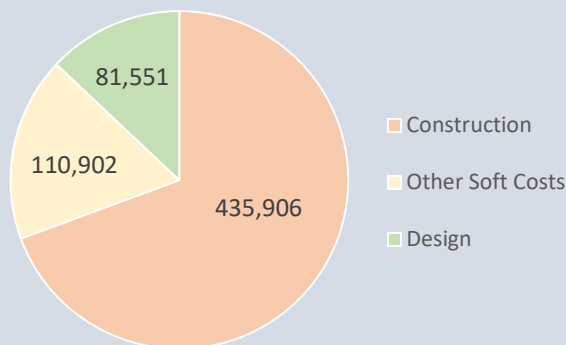

MONTHLY/CUMULATIVE COST

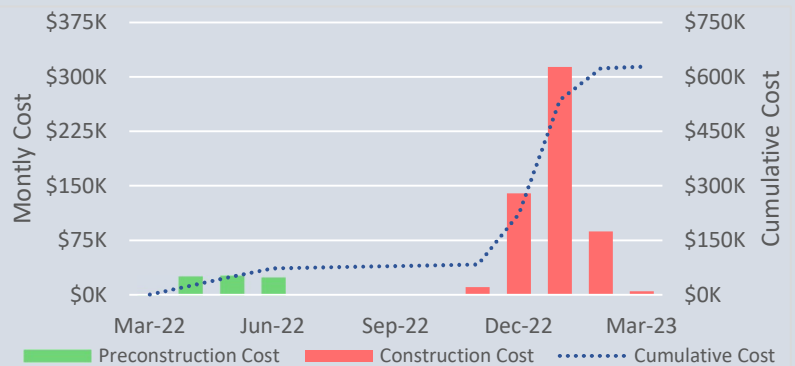

PROJECT SCHEDULE

	Feb-22	Mar-22	Jul-22	Aug-22	Sep-22	Dec-22	Jan-23	Apr-23
Design	Mar-22	Jul-22						
DSA	Jul-22	Oct-22						
Bid/Award	Jul-22	Nov-22						
Construction	Dec-22	Mar-23						
Close-out	Mar-23	Apr-23						
