
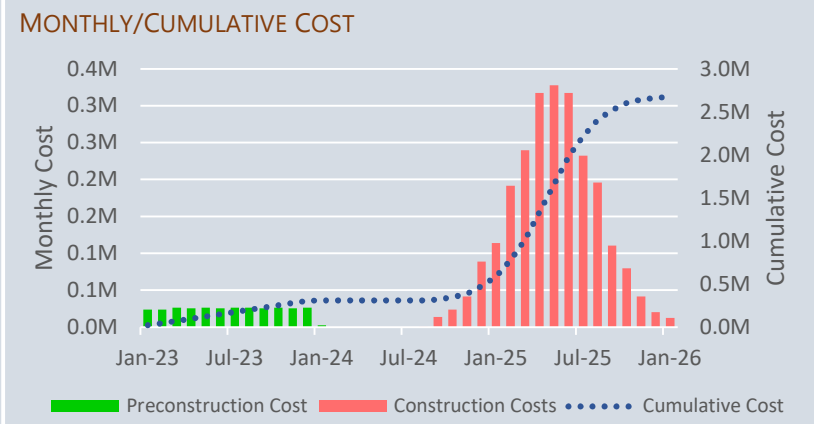


KEMPTON

SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	<ul style="list-style-type: none"> Security Improvements Improvements in School Grounds Accessibility Upgrades
PROJECT NUMBER	9404	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	D	CONTRACTOR	TBD	
PROJECT DELIVERY	TBD	INSPECTOR	Pending Selection	
SITE LOCATION	Online Map Link			

PROJECT FINANCIALS					
PROGRAM FUND	136,235,372	PROJECT COMMITMENTS	232,070	COST TO DATE	24,469
PROJECT BUDGET	2,676,367	% COMMITTED	8.67%	REMAINING BUDGET	2,444,297

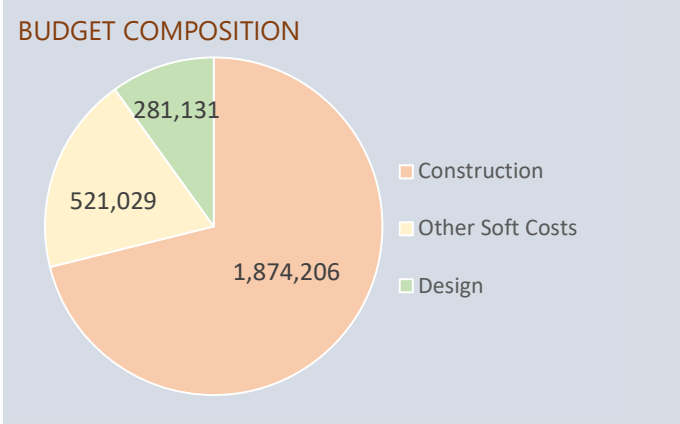

PROJECT SCHEDULE

Phase	Start	End
Design	Jul-22	Jun-23
DSA	Jun-23	Aug-23
Bid/Award	Aug-23	Dec-23
Construction	Dec-23	Jun-25
Close-out	Jun-25	Jul-25
