





# LA MESA ARTS ACADEMY

## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9201	ARCHITECT	Studio-WC	
PROJECT BUNDLE	C	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	136,235,372	PROJECT COMMITMENTS	464,170	COST TO DATE	123,044
PROJECT BUDGET	5,075,454	% COMMITTED	9.15%	REMAINING BUDGET	4,611,284

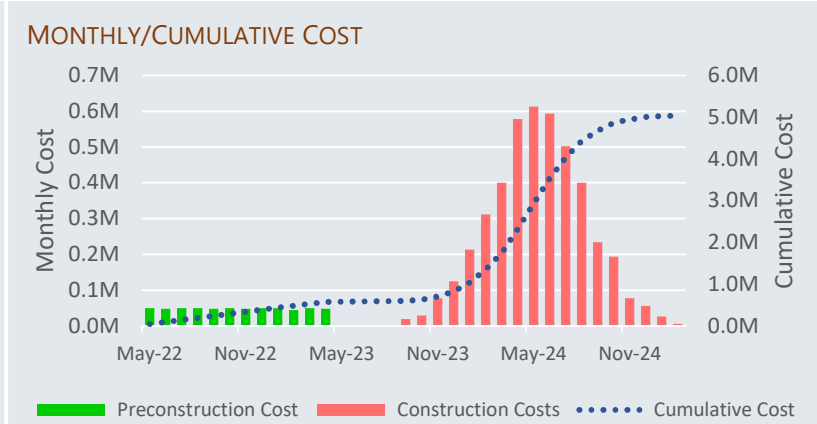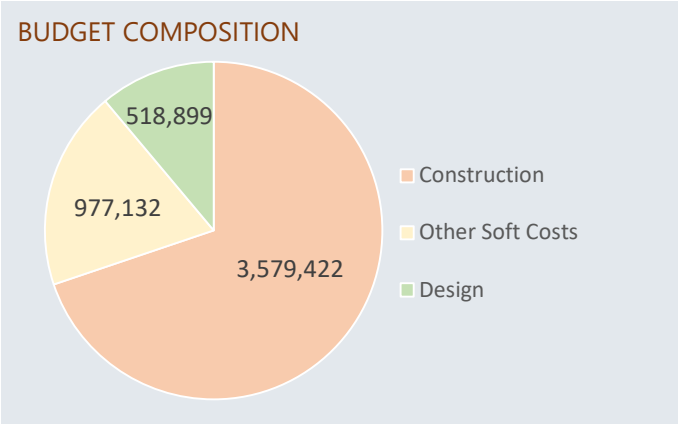

### PROJECT SCHEDULE

Activity	Start	End
Design	Sep-22	Sep-23
DSA	Sep-23	Dec-23
Bid/Award	Dec-23	Apr-24
Construction	Apr-23	Oct-25
Close-out	Oct-25	Nov-25
