





# LA PRESA

## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9405	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	D	CONTRACTOR	TBD	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	136,235,372	PROJECT COMMITMENTS	355,880	COST TO DATE	35,790
PROJECT BUDGET	4,987,447	% COMMITTED	7.14%	REMAINING BUDGET	4,631,567

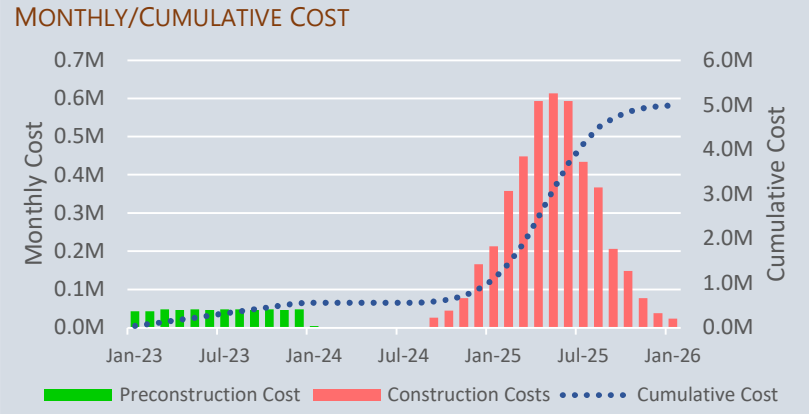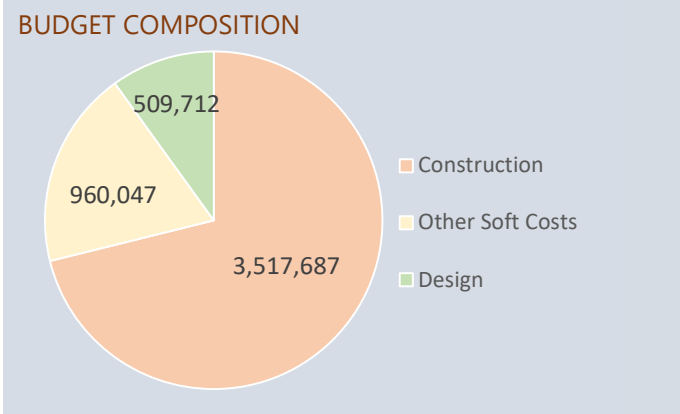

### PROJECT SCHEDULE

Activity	Start	End
Design	Jul-22	Jun-23
DSA	Jun-23	Aug-23
Bid/Award	Aug-23	Dec-23
Construction	Dec-23	Jun-25
Close-out	Jun-25	Jul-25

