





# MURRAY MANOR

## SITE IMPROVEMENTS



PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9103	ARCHITECT	Pending Selection	
PROJECT BUNDLE	E	CONTRACTOR		
PROJECT DELIVERY	TBD	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	136,235,372	PROJECT COMMITMENTS	39,300	COST TO DATE	11,988
PROJECT BUDGET	2,273,753	% COMMITTED	1.73%	REMAINING BUDGET	2,234,453

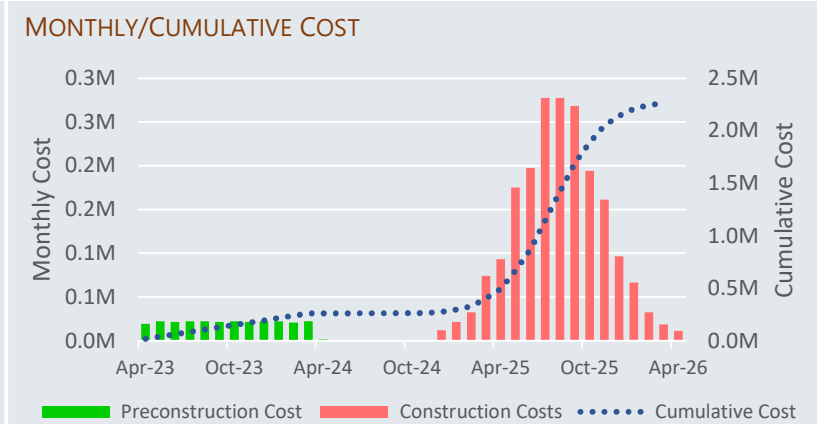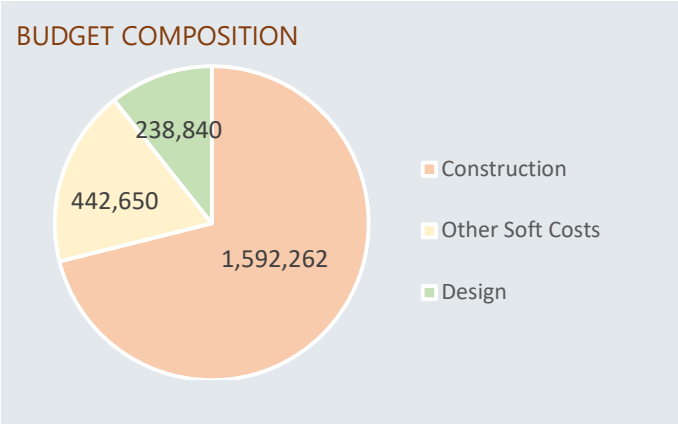

### PROJECT SCHEDULE

Activity	Start	End
Design	Feb-23	Feb-24
DSA	Feb-24	Jun-24
Bid/Award	Jun-24	Oct-24
Construction	Oct-24	Mar-26
Close-out	Mar-26	Apr-26

