



PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9205	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	A	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	Online Map Link			


RENDERINGS/AREAS RECEIVING IMPROVEMENT

Graphics signage concept

Damaged wall lettering

Entrance Rendering

PROJECT FINANCIALS				
PROGRAM FUND	136,235,372	PROJECT COMMITMENTS	-	COST TO DATE 48,185
PROJECT BUDGET	776,247	% COMMITTED	-	REMAINING BUDGET -

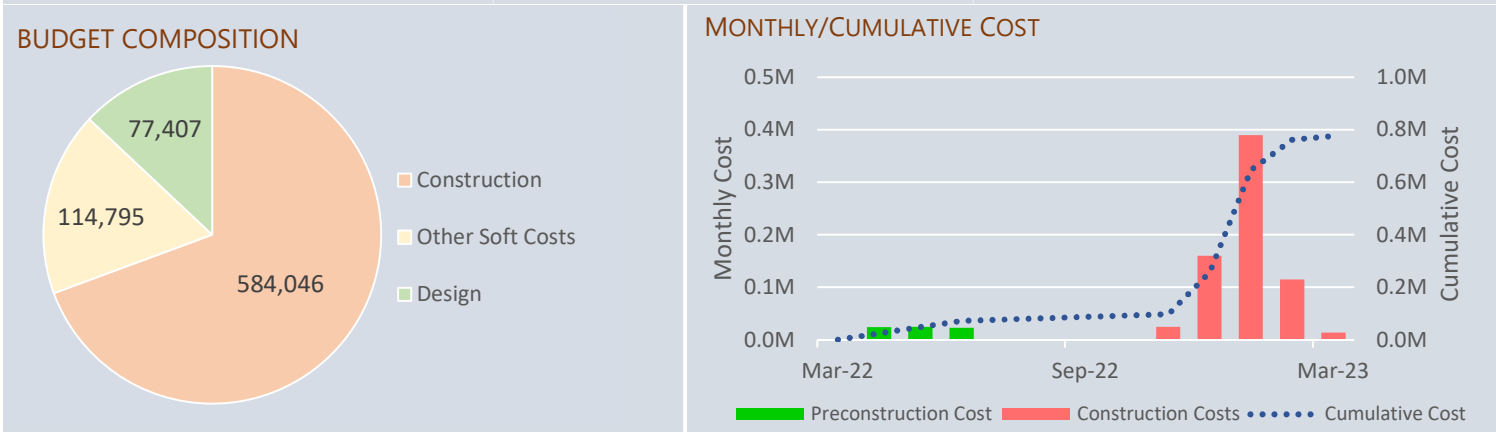

PROJECT SCHEDULE	Feb-22	Mar-22	May-22	Jun-22	Aug-22	Sep-22	Nov-22	Dec-22	Feb-23
Design									
DSA									
Bid/Award									
Construction									
Close-out									
