



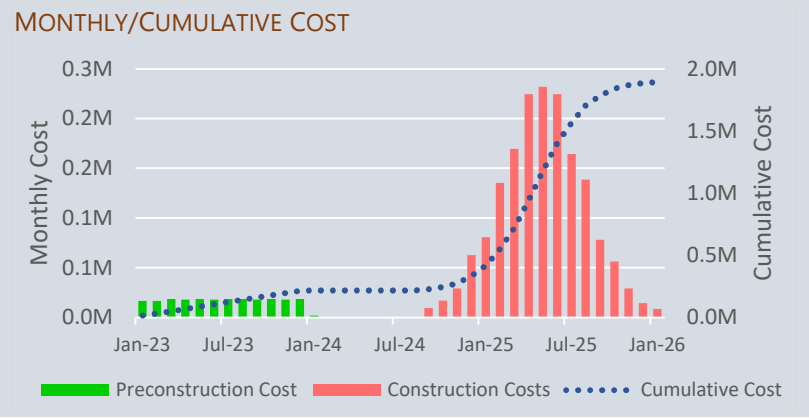

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9403	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	D	CONTRACTOR	TBD	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

Suggested site improvements include entry modernization work including a new pole mounted digital marquee, landscaping, decorative fencing, and required ADA work if needed after surveys have been completed, security fencing along the site perimeter, removal of two buildings at the rear of the campus, and landscape improvements overgrown campus garden at the front of the campus.

PROJECT FINANCIALS					
PROGRAM FUND	136,000,000	PROJECT COMMITMENTS	183,094	COST TO DATE	33,855
PROJECT BUDGET	1,893,596	% COMMITTED	9.67%	REMAINING BUDGET	1,710,501

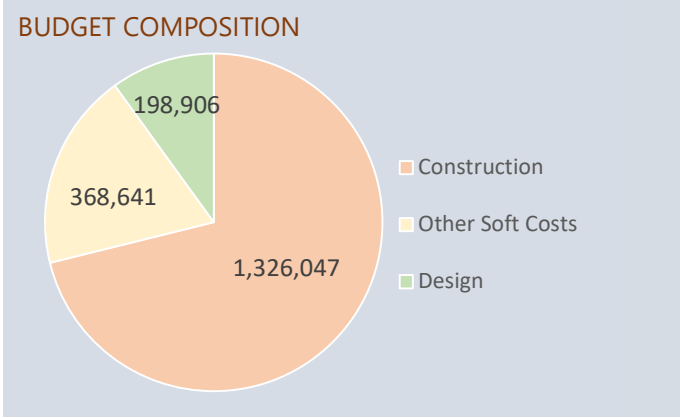

### PROJECT SCHEDULE

Activity	Start	End
Design	Jul-22	Jun-23
DSA	Jun-23	Aug-23
Bid/Award	Aug-23	Dec-23
Construction	Dec-23	Jun-25
Close-out	Jun-25	Jul-25

