



# LOMA ELEMENTARY



## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Improvement in School Grounds, Campus Infrastructure Upgrades, Signage/Marquee Upgrades
PROJECT NUMBER	9304	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

### AREAS RECEIVING IMPROVEMENT



PROJECT FINANCIALS					
PROGRAM FUND	136,235,373	PROJECT COMMITMENTS	149,491	COST TO DATE	60,311
PROJECT BUDGET	1,007,071	% COMMITTED	14.84%	REMAINING BUDGET	857,579

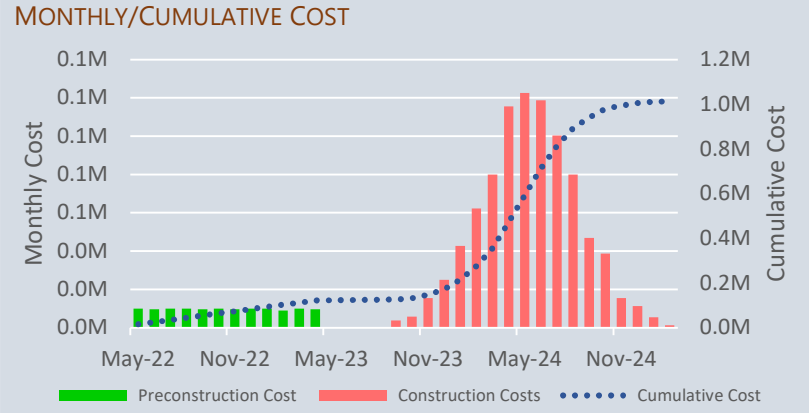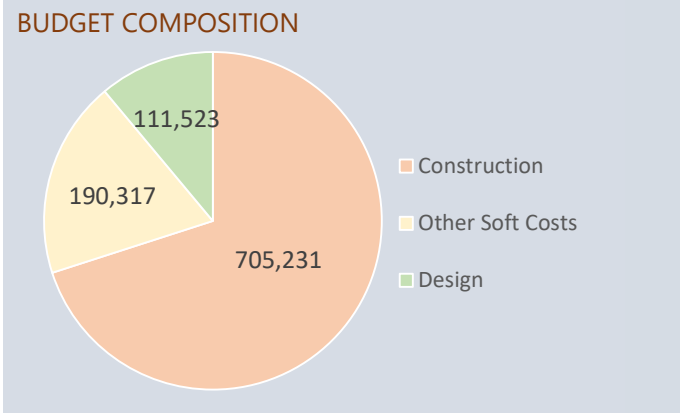

#### PROJECT SCHEDULE

Activity	Start	End
Design	Jun-23	Feb-24
DSA	Feb-24	Aug-24
Bid/Award	Aug-24	Nov-24
Construction	Nov-24	Oct-25
Close-out	Oct-25	Nov-25

