





PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Campus Infrastructure Upgrades & Signage/Marquee Upgrades
PROJECT NUMBER	9302	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	Online Map Link			

AREAS RECEIVING IMPROVEMENT



PROJECT FINANCIALS					
PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	441,916	COST TO DATE	309,738
PROJECT BUDGET	3,754,237	% COMMITTED	12%	REMAINING BUDGET	132,178

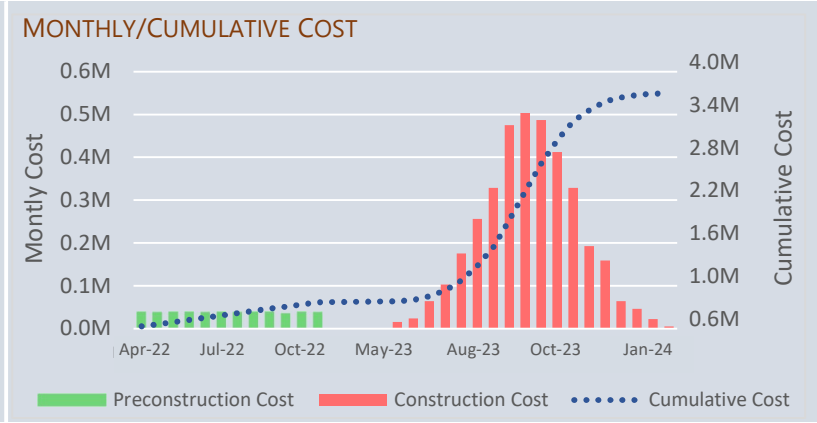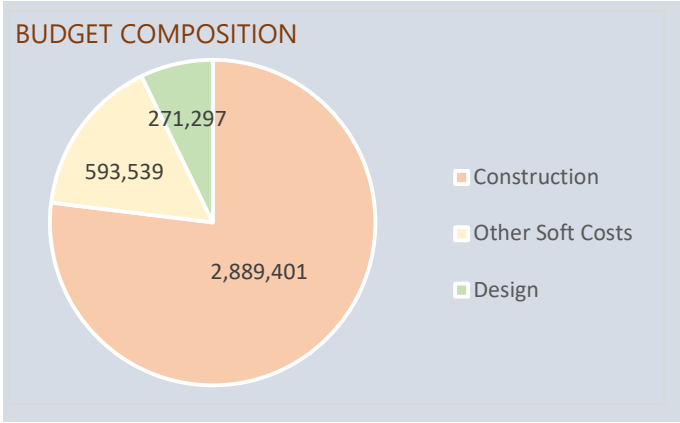

PROJECT SCHEDULE

Task Name	Duration	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	
Design	213 days	[Gantt bar spanning from start to end]												
DSA	37 days	[Gantt bar spanning from start to end]												
Bid/Award	36 days	[Gantt bar spanning from start to end]												
Construction	396 days	[Gantt bar spanning from start to end]												
Close-Out	22 days	[Gantt bar spanning from start to end]												

