



# MURDOCK ELEMENTARY

## SITE IMPROVEMENTS



PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Improvement in School Grounds, Cooling Tower HVAC & Signage/Marquee Upgrades
PROJECT NUMBER	9305	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

### AREAS RECEIVING IMPROVEMENT



### PROJECT FINANCIALS

PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	228,053	COST TO DATE	148,550
PROJECT BUDGET	2,853,104	% COMMITTED	8%	REMAINING BUDGET	79,503

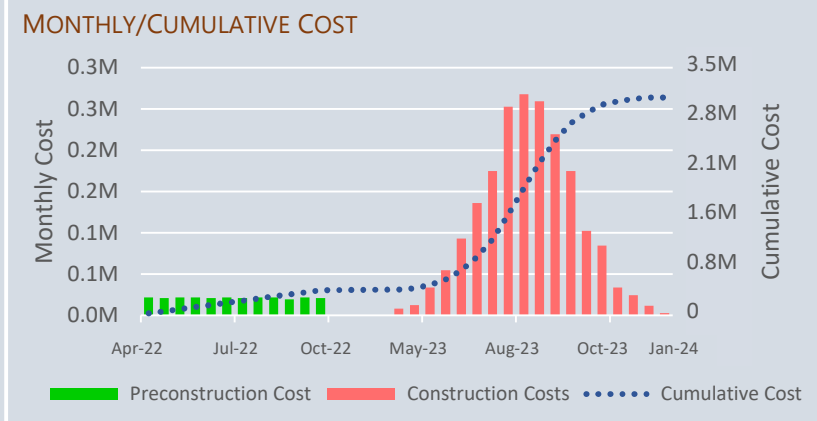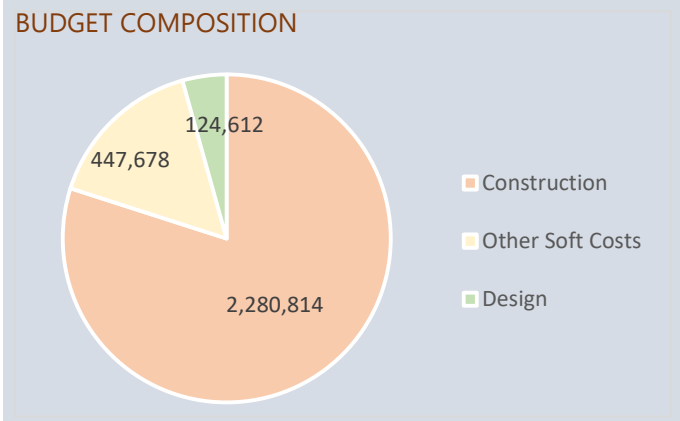

### PROJECT SCHEDULE

Task Name	Duration	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
Design	213 days	█											
DSA	37 days				█								
Bid/Award	36 days					█							
Construction	396 days						█						
Close-Out	22 days											█	

