



STEAM ACADEMY

SLOPE STABILIZATION

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Closeout	PROJECT MGR.	Paul Cristilli (Kitchell)	Mitigation of the slope as recommended in the geotechnical evaluation which includes the removal of existing clay soils replacing with stabilization to correct the slope stability.
PROJECT NUMBER	9407	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	A	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	n/a	
SITE LOCATION	Online Map Link			


AERIAL PROGRESS PHOTOS




PROJECT FINANCIALS

PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	2,282,330	COST TO DATE	2,076,388
PROJECT BUDGET	6,560,841	% COMMITTED	35%	REMAINING BUDGET	4,278,511

BUDGET COMPOSITION

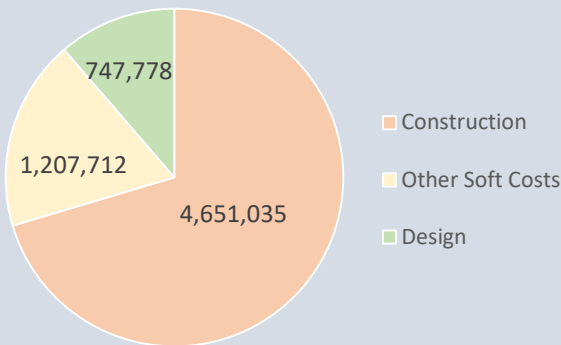

MONTHLY/CUMULATIVE COST

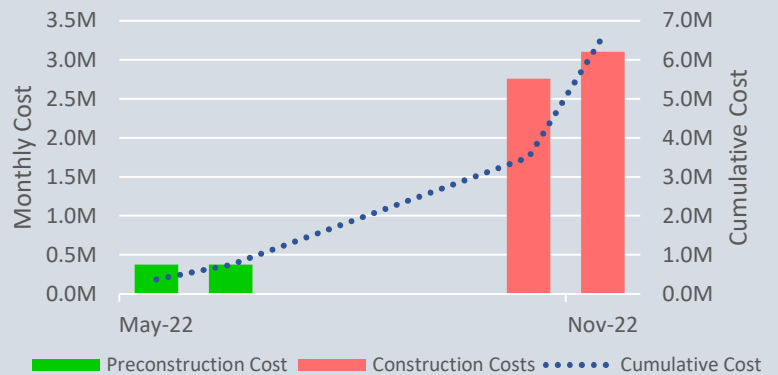

PROJECT SCHEDULE

Task Name	Duration	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	2023	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
Design	58 days	[Gantt bar from May to July]																	
Bid/Award	39 days	[Gantt bar from July to October]																	
Construction	76 days	[Gantt bar from September to May]																	
Close-Out	179 days	[Gantt bar from May to September]																	
