



MURDOCK ELEMENTARY

SITE IMPROVEMENTS



PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Improvement in School Grounds, Cooling Tower HVAC & Signage/Marquee Upgrades, Trash Enclosure
PROJECT NUMBER	9305	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	Online Map Link			

AREAS RECEIVING IMPROVEMENT



PROJECT FINANCIALS

PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	2,204,680	COST TO DATE	522,940
PROJECT BUDGET	2,853,104	% COMMITTED	77%	REMAINING BUDGET	648,424

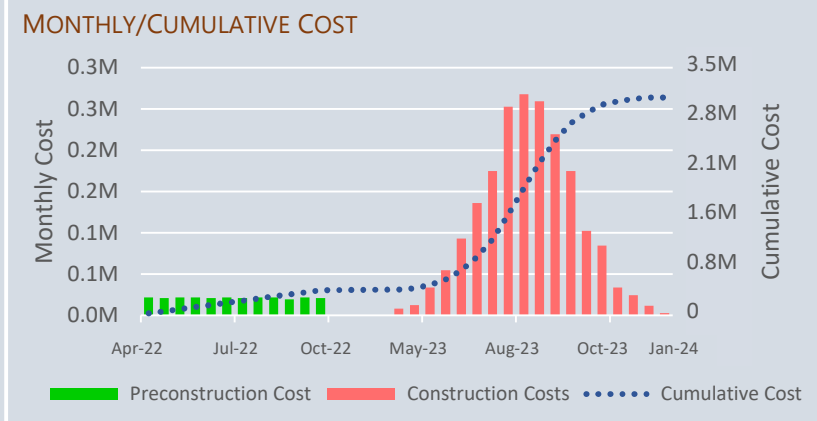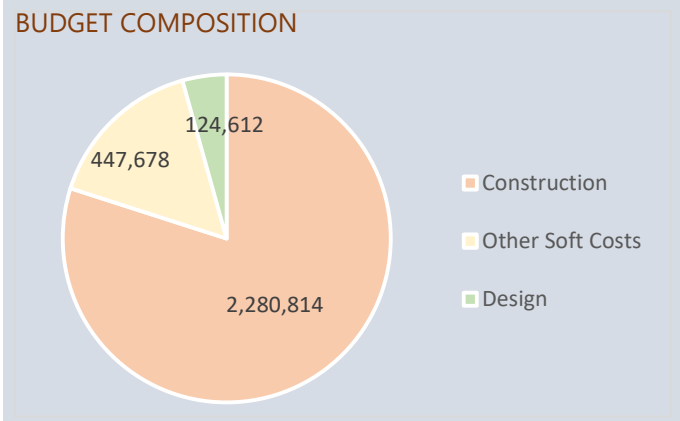

PROJECT SCHEDULE

Task Name	Duration	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025
Design	213 days	█											
DSA	37 days				█								
Bid/Award	36 days					█							
Construction	396 days						█						
Close-Out	22 days											█	

