





# NORTHMONT

## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE Security Improvements, Improvement in School Grounds, Accessibility Upgrades Campus Infrastructure Upgrades and Signage/Marquee Upgrades, Trash Enclosure.
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9104	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	E	CONTRACTOR	Pending Selection	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	381,213	COST TO DATE	108,212
PROJECT BUDGET	5,411,171	% COMMITTED	7%	REMAINING BUDGET	5,029,958

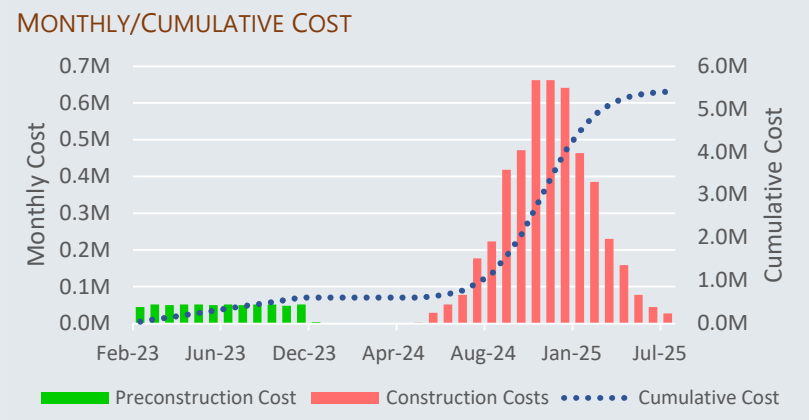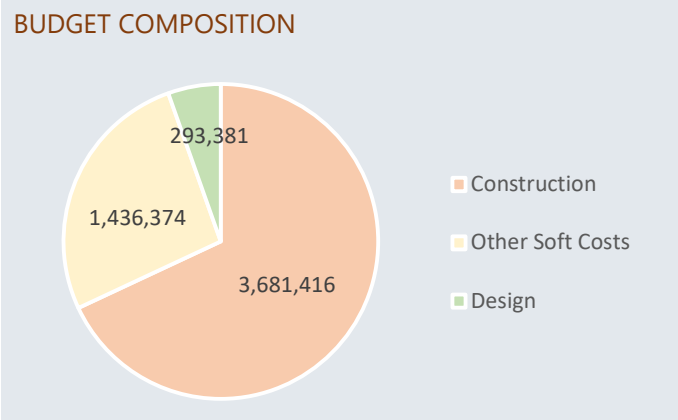

### PROJECT SCHEDULE

Task Name	Duration	Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025		
		Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
Design	229 days	[Active]																													
DSA	71 days																														
Bid/Award	42 days																														
Construction	262 days																														
Close-Out	22 days																														

