





# MARYLAND AVENUE

## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Campus Infrastructure Upgrades & Signage/Marquee Upgrades
PROJECT NUMBER	9105	ARCHITECT	Studio-WC	
PROJECT BUNDLE	C	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	137,064,475	PROJECT COMMITMENTS	222,923	COST TO DATE	120,982
PROJECT BUDGET	1,669,319	% COMMITTED	13%	REMAINING BUDGET	1,446,396

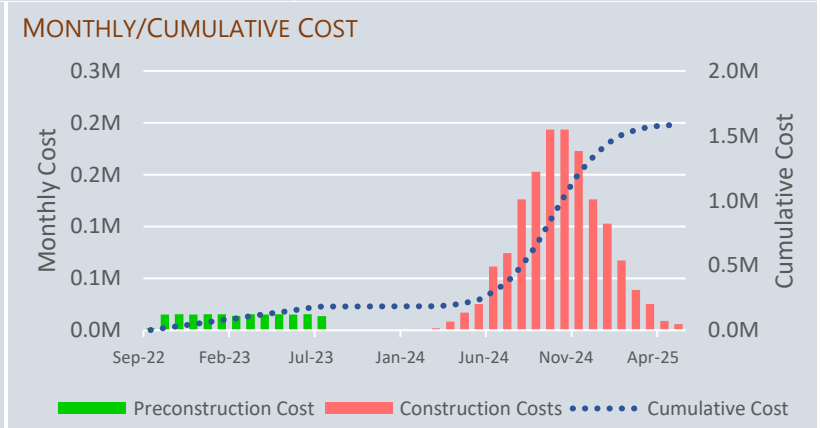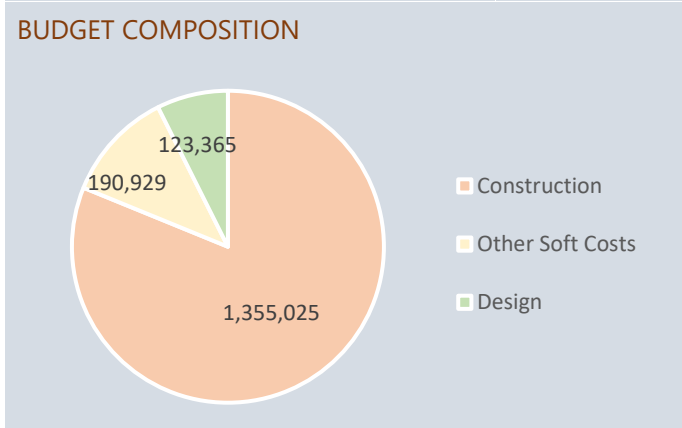

### PROJECT SCHEDULE

Task Name	Duration	022	Qtr 4, 2022	Qtr 3, 2023	Qtr 2, 2023	Qtr 1, 2023	Qtr 4, 2023	Qtr 3, 2024	Qtr 2, 2024	Qtr 1, 2024	Qtr 4, 2024	Qtr 3, 2024	Qtr 2, 2024	Qtr 1, 2025								
		Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	
Design	245 days																					
DSA	105 days																					
Bid/Award	41 days																					
Construction	261 days																					
Close-Out	22 days																					

