





# MURRAY MANOR

## SITE IMPROVEMENTS



PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9103	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	E	CONTRACTOR	Lusardi	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS			
PROGRAM FUND	137,064,475	PROJECT COMMITMENTS	165,732
PROJECT BUDGET	3,273,753	% COMMITTED	5%
		COST TO DATE	80,119
		REMAINING BUDGET	3,108,022

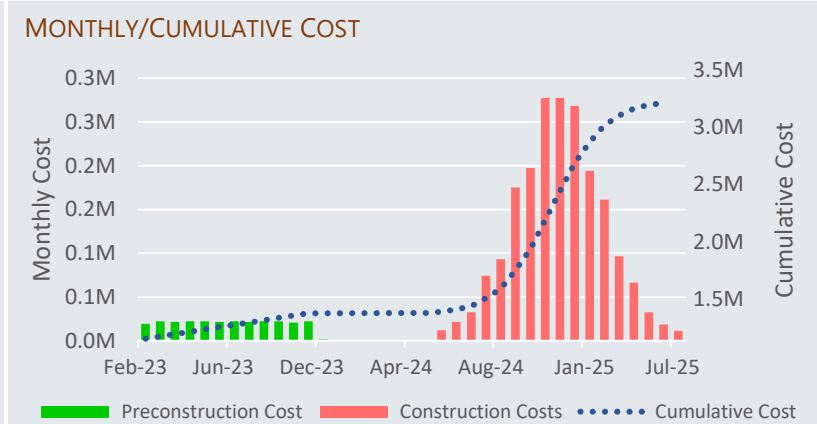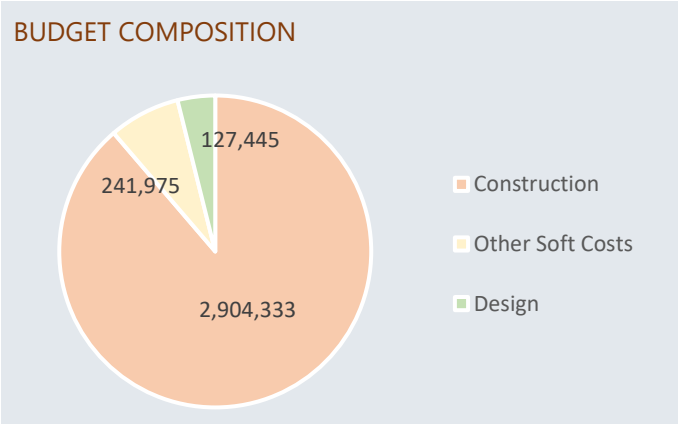

### PROJECT SCHEDULE

Task Name	Duration	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	Qtr 4, 2023	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025
Design	229 days	█				█		█		█	
DSA	71 days	█		█		█		█		█	
Bid/Award	42 days	█		█		█		█		█	
Construction	262 days	█		█		█		█		█	
Close-Out	22 days	█		█		█		█		█	

