





# BANCROFT

## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9403	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	D	CONTRACTOR	Lusardi	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

Suggested site improvements include entry modernization work including a new pole mounted digital marquee, landscaping, decorative fencing, trash enclosure and required ADA work if needed after surveys have been completed, security fencing along the site perimeter, removal of two buildings at the rear of the campus, and landscape improvements overgrown campus garden at the front of the campus.

PROJECT FINANCIALS			
PROGRAM FUND	137,064,475	PROJECT COMMITMENTS	\$296,005
PROJECT BUDGET	1,850,271	% COMMITTED	16%
		COST TO DATE	168,768
		REMAINING BUDGET	1,554,267

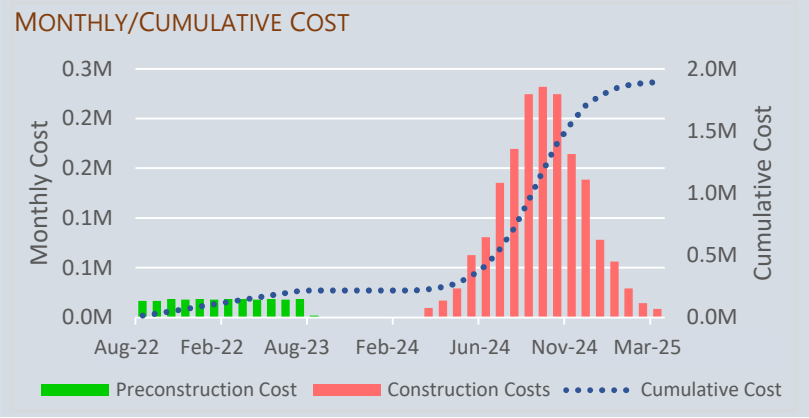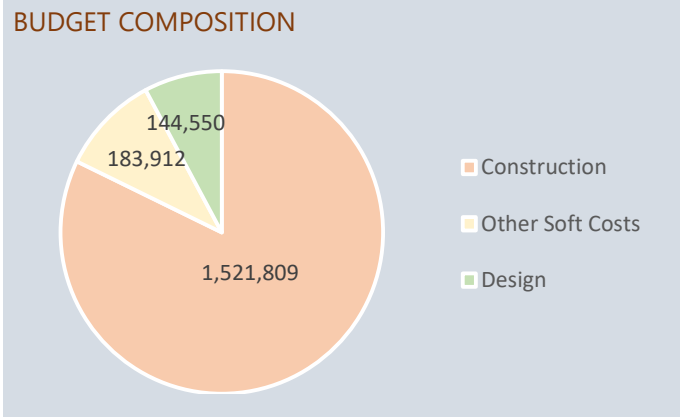

### PROJECT SCHEDULE

Task Name	Duration	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
Design	281 days	[Progress bar]																							
DSA	50 days	[Progress bar]																							
Bid/Award	54 days	[Progress bar]																							
Construction	118 days	[Progress bar]																							
Close-Out	22 days	[Progress bar]																							

