



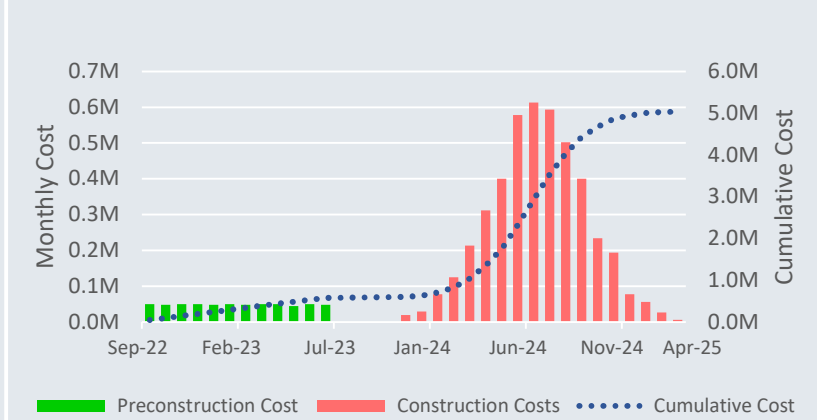

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Campus Infrastructure Upgrades & Signage/Marquee Upgrades, Trash Enclosure
PROJECT NUMBER	9201	ARCHITECT	Studio-WC	
PROJECT BUNDLE	C	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	Online Map Link			

PROJECT FINANCIALS					
PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	737,928	COST TO DATE	577,035
PROJECT BUDGET	5,860,487	% COMMITTED	13%	REMAINING BUDGET	5,122,560

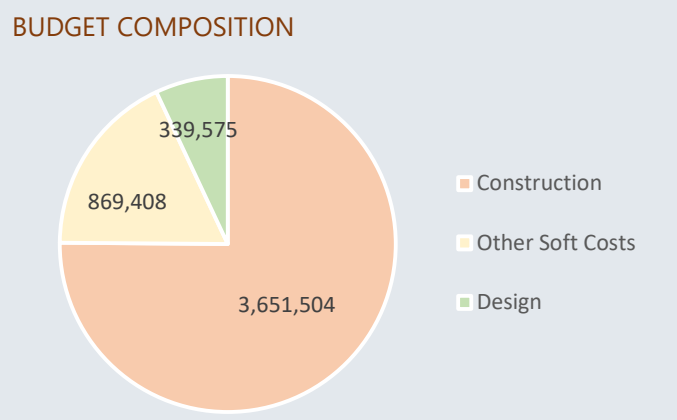

PROJECT SCHEDULE

Task Name	Duration	2022	2023	2024	2025																		
		Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
Design	245 days																						
DSA	105 days																						
Bid/Award	41 days																						
Construction	261 days																						
Close-Out	22 days																						
