



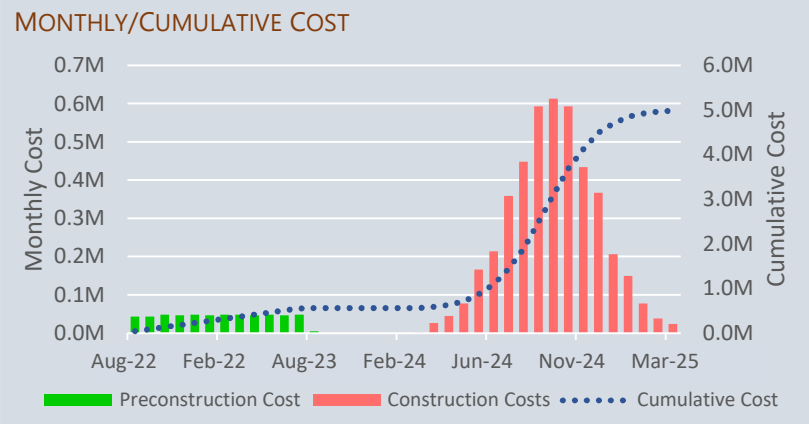

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9405	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	D	CONTRACTOR	Lusardi	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	Online Map Link			

Suggested site improvements include security fencing at select locations, asphalt sealcoating and paving in the play field courts, workout equipment in the play area, replacement of the chillers and hydronic piping on campus, trash enclosure and concrete plaza and sidewalk improvements as necessary and critical infrastructure.

PROJECT FINANCIALS					
PROGRAM FUND	137,064,475	PROJECT COMMITMENTS	689,807	COST TO DATE	342,219
PROJECT BUDGET	4,880,365	% COMMITTED	14%	REMAINING BUDGET	4,190,558

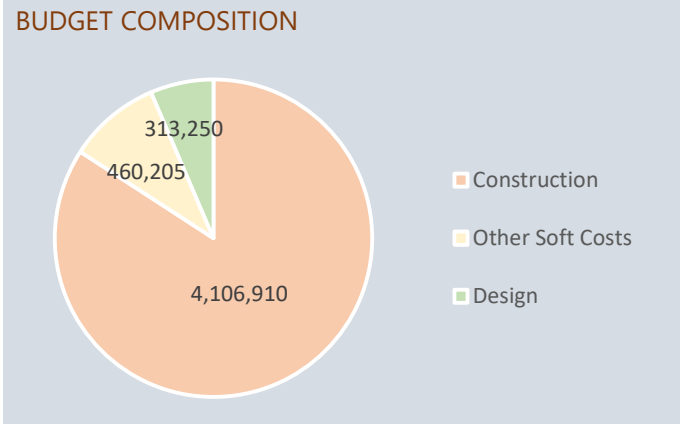

PROJECT SCHEDULE

Task Name	Duration	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep		
Design	281 days	[Bar]																					
DSA	50 days																						
Bid/Award	54 days																						
Construction	119 days																						
Close-Out	22 days																						

