





# MURDOCK ELEMENTARY

## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Improvement in School Grounds, Cooling Tower HVAC & Signage/Marquee Upgrades, Trash Enclosure
PROJECT NUMBER	9305	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	137,064,475	PROJECT COMMITMENTS	2,320,132	COST TO DATE	1,289,372
PROJECT BUDGET	2,653,104	% COMMITTED	87%	REMAINING BUDGET	332,972

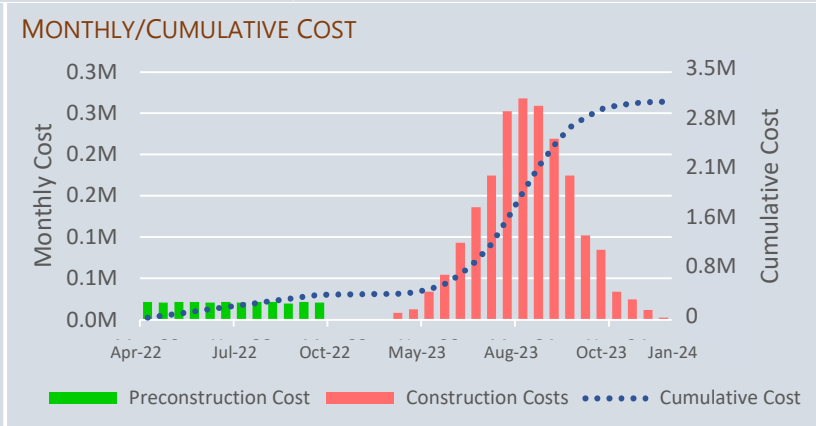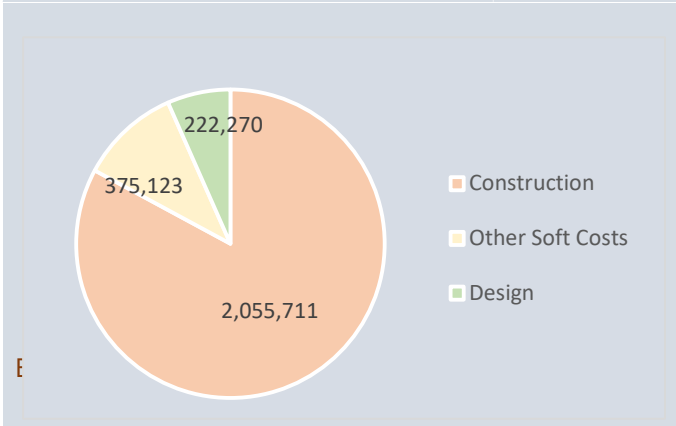

Task Name	Duration	Qtr 2, 2022			Qtr 3, 2022			Qtr 4, 2022			Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024				
		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
Design	213 days	[Bar chart showing Design task duration from Mar 2022 to Jan 2023]																												
DSA	23 days																													
Bid/Award	64 days																													
Construction	209 days																													
Close-Out	23 days																													
