





MURDOCK ELEMENTARY

SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Improvement in School Grounds, Cooling Tower HVAC & Signage/Marquee Upgrades, Trash Enclosure
PROJECT NUMBER	9305	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	Online Map Link			

PROJECT FINANCIALS					
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	2,324,796	COST TO DATE	2,133,553
PROJECT BUDGET	2,653,104	% COMMITTED	88%	REMAINING BUDGET	328,308

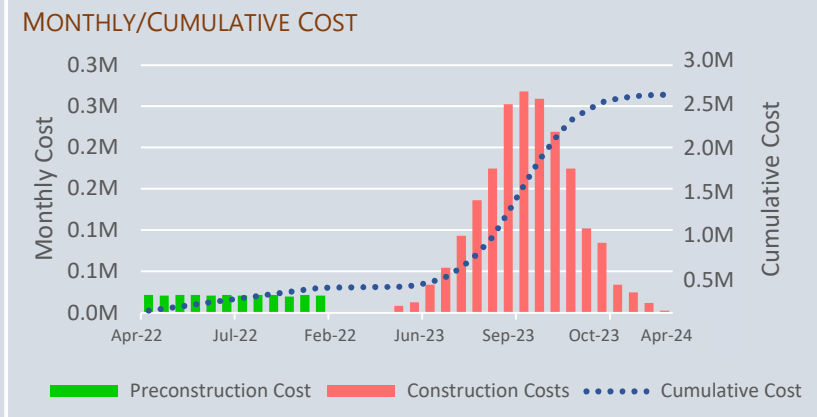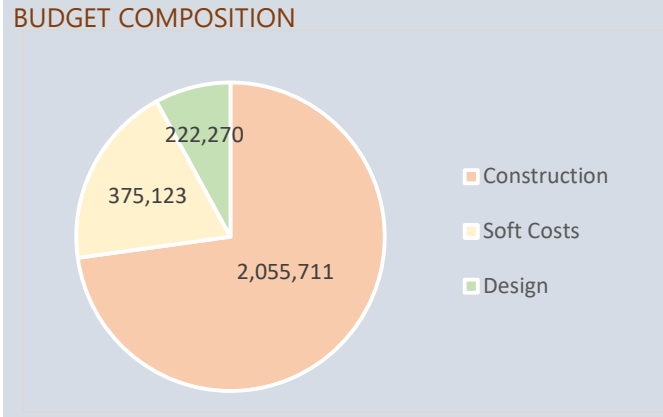

PROJECT SCHEDULE

Task Name	Duration	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug		
Design	213 days	[Bar]																							
DSA	23 days				[Bar]																				
Bid/Award	64 days					[Bar]																			
Construction	271 days?								[Bar]																
Close-Out	22 days																						[Bar]		

