



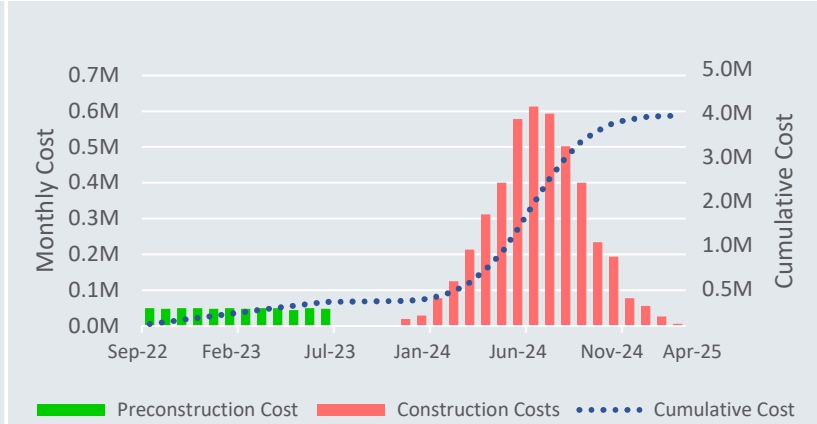

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE Security Improvements, Accessibility Upgrades, Campus Infrastructure Upgrades & Signage/Marquee Upgrades, Trash Enclosure
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9201	ARCHITECT	Studio-WC	
PROJECT BUNDLE	C	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS			
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	3,156,506
PROJECT BUDGET	3,889,258	% COMMITTED	81%
		COST TO DATE	1,218,783
		REMAINING BUDGET	732,752

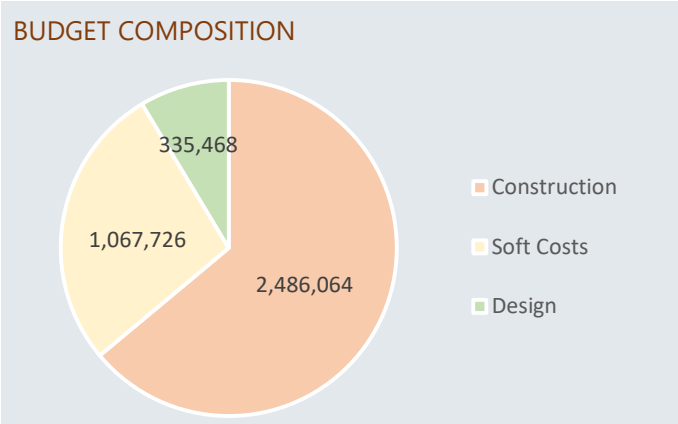

### PROJECT SCHEDULE

Task Name	Duration	Start	End
Design	245 days	Aug-22	Jan-24
DSA	105 days	Jul-23	Aug-23
Bid/Award	41 days	Feb-24	Mar-24
Construction	261 days	Mar-24	Jan-25
Close-Out	22 days	Dec-24	Jan-25
