
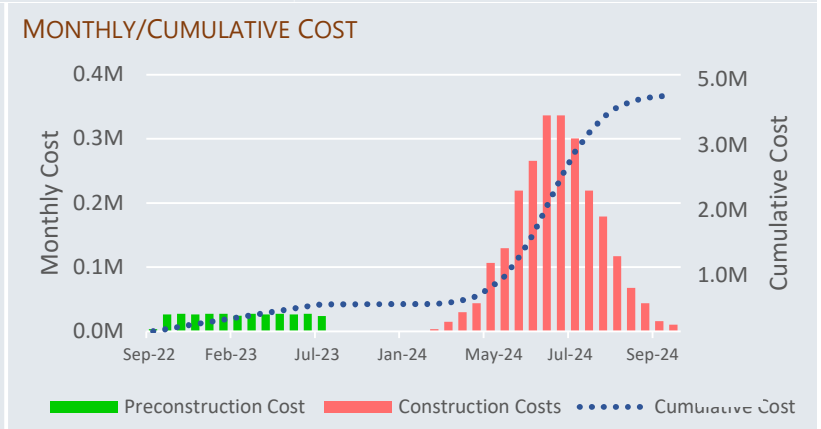


ROLANDO

SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Shade Improvements, Campus Infrastructure Upgrades & Signage/Marquee Upgrades, Trash Enclosure
PROJECT NUMBER	9204	ARCHITECT	Studio-WC	
PROJECT BUNDLE	C	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	Online Map Link			

PROJECT FINANCIALS					
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	3,809,172	COST TO DATE	233,573
PROJECT BUDGET	4,430,338	% COMMITTED	86%	REMAINING BUDGET	621,166

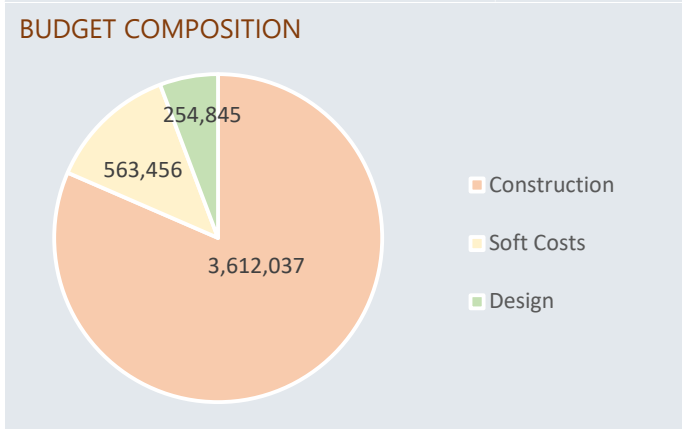

PROJECT SCHEDULE

Task Name	Duration	Start	End
Design	245 days	Aug-22	Jan-23
DSA	105 days	Oct-23	Jan-24
Bid/Award	41 days	Jan-24	Mar-24
Construction	261 days	Mar-24	Jan-25
Close-Out	22 days	Dec-24	Jan-25

