Measure V Bond Program



#### Overview

This report covers the period from May 2022 through July 2022.

Highlights of Activity during the period include:

- Presentation of Measure V update Board Meeting May 10, 2022.
- Citizens' Bond Oversight Committee meeting held May 18, 2022.
- Board approved Lease-Leaseback (LLB) developer for Bundle A
  - STEAM slope stabilization
  - Entrance improvements at STEAM Academy, LMAAC, Spring Valley Academy and Parkway Middle School
  - LLB developer started trade contractor advertising/procurement process
- Initiated quick start campus security improvements
  - Fence and gate improvements at 4 sites
  - Main entrance video/gate control system at 19 sites

#### **COVID-19 Impacts**

Bond program planning, design and construction continues on-schedule with both in-person and virtual collaboration meetings. Field work continues with supporting construction management and architect/engineering and inspection personnel.

Contractors and developers shall comply with all applicable federal, state and local laws regarding COVID-19 at contractor/developer sole expense, and contractor/developer will provide the District with written verification of such compliance.

#### **Projects in Construction:**

Quick start campus security improvements

#### **Projects in Design and Construction Document development:**

Bundles B, C, and D (18 sites)

#### Projects submitted to Division of State Architect for Review/Approval

• Bundle A: Steam Slope Stabilization Middle School Entrance Modernization

#### Project completed/closeout

• LMAAC Abatement

Measure V Bond Program



#### Overview

#### **Board Adopted Program and Projects Baseline Budgets**

#### 14 December 2021

Budgets shown are initial, baseline budgets, and include design, engineering, construction, inspection, testing and construction management. Additional costs are included as appropriate for each site. Budgets also include contingencies for escalation, changes, and unforeseen conditions.

Project scopes and designs will be developed in more detail as Architects and Engineers are assigned to each site and project grouping. As a result, initial baseline budgets are expected to change over time.

ELEMEI	NTARY SCHOOLS	
Avond	ale	2,640,854
	Single point of access and fencing improvements School entrance modernization ADA upgrades	
Bancro	oft	1,893,596
	Single point of access and fencing improvements School entrance modernization ADA upgrades	
Casa D	De Oro	4,121,685
	Sewer line replacement, as needed Storm drain system replacement, as needed Single point of access and fencing improvements School entrance modernization ADA upgrades	
Fletche	er Hills	4,142,269
	Administration access improvements Single point of access and fencing improvements School entrance modernization ADA upgrades	
Highla	nds	1,602,954
	Single point of access and fencing improvements School entrance modernization ADA upgrades	

### LA MESA-SPRING VALLEY SCHOOLS Measure V Bond Program



#### Overview

ELEMENTARY SCHOOLS	
Kempton 2,6	576,367
Single point of access and fencing improvements	
School entrance modernization	
ADA upgrades	
	197,138
Convert Administration Office to Library	
Convert Library to Interim Administration	
Improve safety of student dropoff zone	
Single point of access and fencing improvements	
Campus entry & wayfinding	
School entrance modernization	
ADA upgrades	
	87,447
Replace cooling tower	
Storm drain system replacement, as needed	
Sewer line replacement, as needed	
Single point of access and fencing improvements	
School entrance modernization	
ADA upgrades	
Lemon 1,7	751,736
Single point of access and fencing improvements	
School entrance modernization	
ADA upgrades	
Loma 7	782,071
Water tank removal	
School entrance modernization	
ADA upgrades	
Maryland 1,5	84,914
Single point of access and fencing improvements	
School entrance modernization	
ADA upgrades	
Murdock 1,6	559,840
Single point of access and fencing improvements	
School entrance modernization	
ADA upgrades	

### LA MESA-SPRING VALLEY SCHOOLS Measure V Bond Program



#### Overview

ELEMENTARY SCHOOLS	
Murray Manor 2,273,7	753
Single point of access and fencing improvements	
School entrance modernization	
ADA upgrades	0.7
Northmont 5,408,2	197
Sewer line replacement, as needed	
Storm drain system replacement, as needed	
Single point of access and fencing improvements School entrance modernization	
Tree removal and new landscaping ADA upgrades	
Rancho 2,001,4	112
Single point of access and fencing improvements	14
School entrance modernization	
ADA upgrades	
Rolando 2,755,9	133
Improve safety of student dropoff zone	
Single point of access and fencing improvements	
School entrance modernization	
ADA upgrades	
Sweetwater Springs 5,629,9	40
Tree removal and new landscaping	
Single point of access and fencing improvements	
Sewer line replacement, as needed	
Storm drain system replacement, as needed	
School entrance modernization	
ADA upgrades	
MIDDLE SCHOOLS	
MS Entrance Modernizations 2,513,4	139
Single points of entry, fencing and security	
Visibility and line of sight	
Wayfinding and signage	
Landscaping improvements	

### LA MESA-SPRING VALLEY SCHOOLS Measure V Bond Program



#### Overview

MIDDLE SCHOOLS	
La Mesa Arts Academy	5,568,239
Sewer line replacement	
Campuswide landscaping improvements	
Single point of access and fencing improvements	
West entrance hardscape and access improvements	
ADA upgrades	
Parkway	16,669,083
Storm water system replacement	
Single point of access and fencing improvements	
Administration office relocation	
Campuswide landscaping improvements	
ADA upgrades	
Spring Valley Academy	3,389,591
Sewer line replacement	
Campuswide landscaping improvements	
Single point of access and fencing improvements	
ADA upgrades	
STEAM at La Presa	4,621,369
Single point of access and fencing improvements	
Replace chillers and gas lines	
Campuswide landscaping improvements	
ADA upgrades	
(Slope stabilization tracked separately)	
OTHER DISTRICT SITES	
Additional Projects	
Slope stabilization and playfield repairs, STEAM site	6,606,525
General infrastructure improvements, Districtwide	6,443,079
Energy efficiency projects, Districtwide	10,371,056
Operations Center	2,303,006
Fencing and wayfinding signage	
General infrastructure improvements	
Trailer demolition and building relocation	

Measure V Bond Program



9,855,792

#### Overview

#### **OTHER DISTRICT SITES**

Education Service Center 6,248,616

Replace curtain walls and interior repairs

#### PROGRAM ADMINISTRATION

#### **Program Administration, Services, and Software**

District staff supporting bond program

Legal services

Program services: standard specifications, auditor,

financial software, funding eligibility specialists,

educational specifications, other advisors

Cost of bond issuances

Program management

#### SUMMARY: BOND PROGRAM BASELINE BUDGET

Total project costs

Program administration

Program contingency

Program Reserve

119,144,208


9,855,792

3,000,000

4,000,000

Total Baseline Program Budget 136,000,000

## LA MESA-SPRING VALLEY SCHOOLS Measure V Bond Program






#### Program Budget Summary

Project #	Bundle	Project Name	Current Budget	Committed Costs	Job to Date Costs	Commitment Balance	Remaining Budget
,	2000		A	В	c	D	E
9106	Α	Parkway Middle School Entry Improvements	\$628,359.69	\$62,971.25	\$17,460.00	(A-B) \$565,388.44	(A-C) \$610,899.69
9205	A	LMAAC Middle School Entry Improvements	\$628,359.70	\$67,406.50	\$17,460.00	\$560,953.20	\$610,899.70
9307	A	Spring Valley Academy Middle School Entry Improvements	\$628,359.69	\$64,771.00	\$17,460.00	\$563,588.69	\$610,899.69
9407	Α	STEAM Slope Stabilization	\$6,606,524.75	\$150,093.66	\$59,786.00	\$6,456,431.09	\$6,546,738.75
9408	A	STEAM Academy Middle School Entry Improvements	\$628,359.69	\$67,275.00	\$17,460.00	\$561,084.69	\$610,899.69
3 100	, ,	Sub-total	\$9,119,963.52	\$412,517.41	\$129,626.00	\$8,707,446.11	\$8,990,337.52
9005	В	Operations Center Site Improvements	\$1,908,207.11	\$168,117.42	\$16,330.00	\$1,740,089.69	\$1,891,877.11
9301	В	Spring Valley Academy Site Improvements	\$3,389,591.21	\$270,471.70	\$41,900.54	\$3,119,119.51	\$3,347,690.67
9302	В	Casa de Oro Site Improvements	\$4,121,685.39	\$322,041.83	\$52,437.42	\$3,799,643.56	\$4,069,247.97
9303	В	Highlands Elementary Site Improvements	\$1,602,953.80	\$171,236.44	\$48,056.56	\$1,431,717.36	\$1,554,897.24
9304	В	Loma Elementary Site Improvements	\$1,002,933.80	\$99,520.00	\$31,347.50	\$682,551.17	\$750,723.67
9305	В	Murdock Site Improvements	\$1,659,839.77	\$163,911.86	\$37,325.30	\$1,495,927.91	\$1,622,514.47
9306	В	Sweetwater Springs Site Improvements	\$5,629,939.77	\$407,400.16	\$55,933.45	\$5,222,539.61	\$5,574,006.32
3300		Sub-total	\$19,094,288.22	\$1,602,699.41	\$283,330.77	\$17,491,588.81	\$18,810,957.45
9105	С	Maryland Avenue Site Improvements	\$1,584,913.59	\$1,002,039.41	\$24,110.00	\$1,436,817.38	\$1,560,803.59
9201	С	La Mesa Arts Academy Site Improvements	\$5,568,238.99	\$460,191.72	\$120,667.00	\$5,108,047.27	\$5,447,571.99
9202	C	La Mesa Dale Site Improvements	\$8,497,137.87	\$574,535.89	\$60,365.00	\$7,922,601.98	\$8,436,772.87
9203	C	Lemon Avenue Site Improvements	\$1,751,735.70	\$161,760.34	\$24,110.00	\$1,589,975.36	\$1,727,625.70
9204	С	Rolando Site Improvements	\$2,755,932.66	\$219,584.83	\$24,110.00	\$2,536,347.83	\$2,731,822.66
3201		Sub-total	\$20,157,958.81	\$1,564,168.99	\$253,362.00	\$18,593,789.82	\$19,904,596.81
9401	D	STEAM Academy Site Improvements	\$4,621,369.51	\$343,430.00	\$27,630.00	\$4,277,939.51	\$4,593,739.51
9402	D	Avondale Site Improvements	\$2,640,853.53	\$215,020.00	\$13,861.50	\$2,425,833.53	\$2,626,992.03
9403	D	Bancroft Site Improvements	\$1,893,596.29	\$175,320.00	\$13,861.50	\$1,718,276.29	\$1,879,734.79
9404	D	Kempton Site Improvements	\$2,676,367.30	\$232,070.00	\$15,111.50	\$2,444,297.30	\$2,661,255.80
9405	D	La Presa Site Improvements	\$4,987,447.34	\$355,880.00	\$21,596.50	\$4,631,567.34	\$4,965,850.84
9406	D	Rancho Site Improvements	\$2,001,411.81	\$173,270.00	\$14,111.50	\$1,828,141.81	\$1,987,300.31
		Sub-total	\$18,821,045.78	\$1,494,990.00	\$106,172.50	\$17,326,055.78	\$18,714,873.28
9101	Е	Parkway Middle School Improvements	\$16,669,083.19	\$61,662.69	\$53,462.69	\$16,607,420.50	\$16,615,620.50
9102	E	Fletcher Hills Elementary School	\$4,142,269.06	\$35,420.00	\$2,250.00	\$4,106,849.06	\$4,140,019.06
9103	E	Murray Manor Site Improvements	\$2,273,753.02	\$39,300.00	\$1,125.00	\$2,234,453.02	\$2,272,628.02
9104	E	Northmont Site Improvements	\$5,408,296.52	\$47,791.98	\$5,246.98	\$5,360,504.54	\$5,403,049.54
		Sub-total	\$28,493,401.79	\$184,174.67	\$62,084.67	\$28,309,227.12	\$28,431,317.12
0000	-	Program Common Costs	\$9,855,691.69	\$1,997,258.80	\$1,379,859.65	\$7,858,432.89	\$8,475,832.04
9000	_	Energy Efficiency Projects - Districtwide	\$10,371,056.42	\$10,371,056.42	\$10,371,056.42	\$0.00	\$0.00
9002	-	Operations Center Trailer Demolition	\$65,252.63	\$62,106.00	\$62,106.00	\$3,146.63	\$3,146.63
9003	-	Portable Building	\$329,545.99	\$51,890.74	\$38,176.72	\$277,655.25	\$291,369.27
9004	-	Education Center Site Improvements	\$6,248,616.17	\$0.00	\$0.00	\$6,248,616.17	\$6,248,616.17
9006	-	Infrastructure Repairs - Districtwide	\$6,443,178.98	\$331,085.00	\$0.00	\$6,112,093.98	\$6,443,178.98
-	-	LMSV Contingency & Reserve	\$7,000,000.00	\$0.00	\$0.00	\$7,000,000.00	\$7,000,000.00
		Total	\$136,000,000.00	\$18,071,947.44	\$12,685,774.73	\$117,928,052.56	\$123,314,225.27





#### Program Summary Schedule (Partial Roll-up)

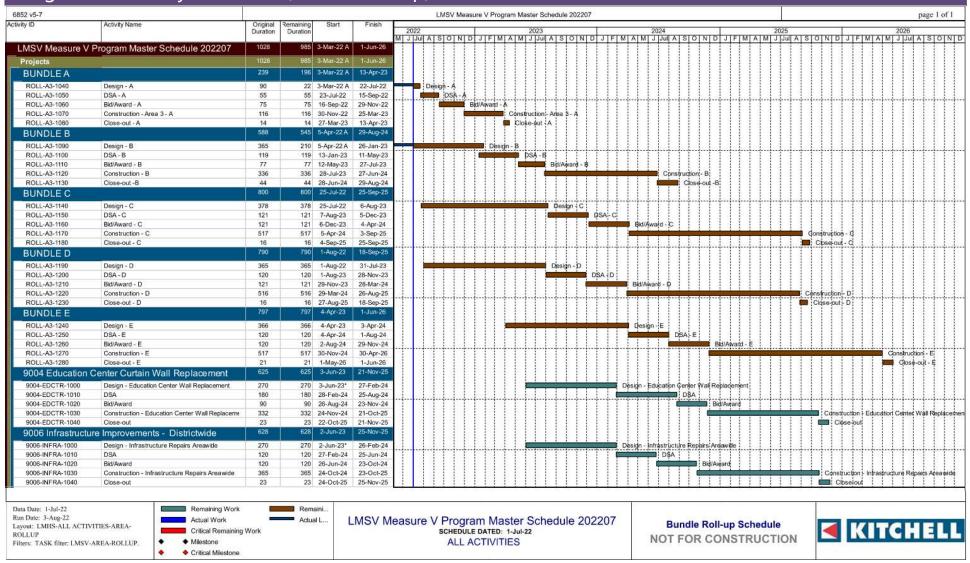

Measure V Bond Program



#### Project Summary - Bundle A

ID	Site(s)	Scope
9106	Parkway Middle School	Entrance Improvements
9205	La Mesa Arts Academy	Entrance Improvements
9408	STEAM Academy	Entrance Improvements
9307	Spring Valley Academy	Entrance Improvements
9407	STEAM Academy	Slope Mitigation

Project Status	
Current Phase	Design
CEQA Status	In Process
DSA Status	Submitted 07/2022
Contract Procurement	LLB RFQ/P Issued April 20 <sup>th</sup> , 2022

Schedule Milestone	Baseline	Current
Design Complete	7/12/2022	7/22/2022
DSA Approval	9/1/2022	9/15/2022
Advertise for Bid	7/29/2022	7/22/2022
Receive Bids	8/26/2022	8/16/2022
Notice of Award	10/4/2022	9/6/2022
Notice to Proceed	10/11/2022	9/7/2022
Final Completion	4/5/2023	3/30/2023
Notice of Completion	4/27/2023	4/28/2023
% Complete STEAM Slope Stabilization	0%	0%
% Complete Parkway Middle School	0%	0%
% Complete La Mesa Arts Academy	0%	0%
% Complete Spring Valley Academy	0%	0%
% Complete STEAM Academy	0%	0%

Design to Budget Amount	\$3,671,112
100% Schematic Design Estimate <sup>1</sup>	\$3,464,976
100% Construction Documents <sup>3</sup>	TBD

<sup>&</sup>lt;sup>1</sup> Schematic Design Estimate should be 90% of Design to Budget Amount.


	ear Critical – Monitor  Risk: STEAM Slope mitigation work will have to be completed on time to avoid rainy
•	Bick: STEAM Slope mitigation work will have to be completed on time to avoid rainy
	season. To expedite the schedule, we will be bidding out the STEAM Slope set upon DSA submittal, and reconcile the changes from DSA upon start of construction.
Critical – Needs Attention	omplete or for Information

#### **Photos/Renderings**



Existing condition pictures of the Slope at the STEAM Academy at La Presa. Mitigation effort of the slope set to commence October 2022.





Parkway Design Recommendations -Mosher Drew Architects



STEAM Design Recommendations -Mosher Drew Architects



LMAAC Design Recommendations -Mosher Drew Architects



Spring Valley Design Recommendations -Mosher Drew Architects

<sup>&</sup>lt;sup>2</sup> Design Development Estimate should be 90% of Design to Budget Amount.

<sup>&</sup>lt;sup>3</sup> Construction Documents estimate should be 95% of Design to Budget Amount

<sup>&</sup>lt;sup>4</sup> Construction Documents estimate should be 93% of Design to Budget Amount



PROJECT INFORM	ATION	PROJECT TEAM		
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9106	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	А	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	Online Map Link			

Current scope to include monument signage, landscaping, hardscaping, marquee signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.

#### AREAS RECEIVING IMPROVEMENT



PROJECT FINANCIALS





# PROGRAM FUND 136,000,000 PROJECT COMMITMENTS PROJECT BUDGET 628,359 COMMITMENT BALANCE BUDGET COMPOSITION 81,551 110,902 435,906 Construction Other Soft Costs \$75 \$0



## PROJECT SCHEDULE Feb-22 Mar-22 May-22 Sep-22 Nov-22 Dec-22 Feb-23 Design DSA Bid/Award Construction



PROJECT INFORMA	ATION	PROJECT TEAM		
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9205	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	А	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	Online Map Link			


Current scope to include monument signage, landscaping, hardscaping, marquee signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.

#### RENDERINGS/AREAS RECEIVING IMPROVEMENT



Design DSA Bid/Award





Feb-23

Jun-22



PROJECT INFORMA	ATION	PROJECT TEAM	Л
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)
PROJECT NUMBER	9408	ARCHITECT	Mosher-Drew
PROJECT BUNDLE	А	CONTRACTOR	Balfour Beatty
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection
SITE LOCATION	Online Map Link		

Current scope to include monument signage, landscaping, hardscaping, marquee signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.

#### AREAS RECEIVING IMPROVEMENT



Design DSA Bid/Award





Feb-23

PROJECT FINANCIALS							
PROGRAM FUND 136,	000,000	PROJECT COMM	IITMENTS	62,275	COST TO DATE		17,460
PROJECT BUDGET	628,359	COMMITMENT E	BALANCE	566,084	REMAINING BUDGET		610,900
BUDGET COMPOSITION			MONTHLY	/CUMULATIVE	COST		
			\$375K				\$750K
81,551			\$300K				\$600K <b>ts</b>
	■ Coı	nstruction	\$225K		:		\$450K
110,902 435,906	Oth	ner Soft Costs	\$150K				\$300K
	■ Des	sign	\$75K			11	\$150K <b>3</b>
			\$0K				\$0K
				Mar-22 Jun econstruction Cos	'	2 Mar-23	
PROJECT SCHEDULE							

Jun-22



#### PROJECT INFORMATION **PROJECT TEAM** Paul Cristilli (Kitchell) PROJECT MGR. PHASE/STATUS Design **ARCHITECT** Mosher-Drew **PROJECT NUMBER** 9307 **PROJECT BUNDLE CONTRACTOR Balfour Beatty Pending Selection** PROJECT DELIVERY Lease-Lease Back **INSPECTOR** SITE LOCATION Online Map Link

#### **PROJECT SCOPE**

Current scope to include monument signage, landscaping, hardscaping, marquee signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.

#### AREAS RECEIVING IMPROVEMENT



Feb-22

Bid/Award

Mar-22





Dec-22

Feb-23

#### PROJECT FINANCIALS **PROGRAM FUND** 136,000,000 **PROJECT COMMITMENTS** 58,200 COST TO DATE PROJECT BUDGET 628,359 570,159 REMAINING BUDGET **COMMITMENT BALANCE** 628,359 MONTHLY/CUMULATIVE COST **BUDGET COMPOSITION** \$375K \$750K 81,551 \$300K \$600K **Montly Cost** Construction \$225K \$450K 110,902 \$300K \$150K **Oran** 435,906 Other Soft Costs \$150K Design \$75K \$0K \$0K Mar-22 Jun-22 Sep-22 Mar-23 Dec-22 Preconstruction Cost Construction Cost ······ Cumulative Cost **PROJECT SCHEDULE**

Jun-22



PROJECT INFORMA	ATION	PROJECT TEAN	1
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)
PROJECT NUMBER	9407	ARCHITECT	Mosher-Drew
PROJECT BUNDLE	А	CONTRACTOR	Balfour Beatty
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection
SITE LOCATION	Online Map Link		

Remediation of the slope as recommended in the geotechnical evaluation which includes the removal of existing clay soils replacing with stabilization to improve the slope stability. Repair existing distressed hardball courts.

#### AREAS RECEIVING IMPROVEMENT







59,786

#### PROJECT FINANCIALS

PROGRAM FUND 136,000,000 PROJECT COMMITMENTS

PROJECT BUDGET 6,606,525 COMMITMENT BALANCE

BUDGET COMPOSITION

MONTH
\$375
\$300
\$1,207,712

Other Soft Costs
\$150
\$75



150,094 COST TO DATE

#### **PROJECT SCHEDULE**

	Feb-22	Mar-22	May-22	Jun-22	Aug-22	Sep-22	Nov-22	Dec-22	Feb-23	
Design										
DSA										
Bid/Award										
Construction										
Close-out										

Measure V Bond Program



#### Quarterly Project Summary - Bundle B

ID	Site(s)	Scope
9005	<b>Operations Center</b>	Site Improvements
9301	Spring Valley Academy	Site Improvements
9302	Casa de Oro	Site Improvements
9303	Highlands Elementary	Site Improvements
9304	Loma Elementary	Site Improvements
9305	Murdock	Site Improvements
9306	Sweetwater Springs	Site Improvements

Project Status	
Current Phase	Design
CEQA Status	
DSA Status	Anticipated Submission: Jan-23
Contract Procurement	

Schedule Milestone	Baseline	Current
Design Complete	01/23/23	01/23/23
DSA Approval	4/6/2023	5/11/2023
Advertise for Bid	5/12/2023	5/12/2023
Receive Bids	TBD	TBD
Notice of Award	7/27/2023	7/27/2023
Notice to Proceed	7/28/2023	7/28/2023
Final Completion	6/28/2024	
Notice of Completion	8/29/2024	8/29/2024
% Complete Operations Center	0%	0%
% Complete Spring Valley Academy	0%	0%
% Complete Casa de Oro	0%	0%
% Complete Highlands	0%	0%
% Complete Loma Elementary	0%	0%
% Complete Murdock	0%	0%
% Complete Sweetwater Springs	0%	0%

Design to Budget Amount	
100% Schematic Design Estimate <sup>1</sup>	9/12/2022
100% Design Development Estimate <sup>2</sup>	11/15/2022
50% Construction Documents <sup>3</sup>	11/16/2022
100% Construction Documents <sup>3</sup>	1/26/2023

- <sup>1</sup> Schematic Design Estimate should be 90% of Design to Budget Amount.
- <sup>2</sup> Design Development Estimate should be 90% of Design to Budget Amount.
- <sup>3</sup> Construction Documents estimate should be 95% of Design to Budget Amount
- <sup>4</sup> Construction Documents estimate should meet the Design to Budget Amount

Issues   Decisions   Risks						
Proceedings as Planned		Near Critical – Monitor				
Critical – Needs Attention		Complete or for Information				

#### **Photos/Renderings**



#### **Proposed Site Plan**

- New 8' decorative metal fence and gate where it occurs New 8' chain ink fence/gate New 4' black vinyl chain link fence/gate Repair fence as necessary

#### Casa De Oro

Design Recommendation provided by Studio WC



provided by Studio WC

**Spring Valley** 

**Design Recommendation** 

provided by Studio WC



- New (2) 10' x 20' Kinder shade

- New (2) 20' x 30' lunch
   structures

- New 8" chain link fence/gate
- New 4" black vinyl chain link fence/gate



#### Murdock Design Recommendation provided by Studio WC



#### PROJECT INFORMATION **PROJECT TEAM** Paul Cristilli (Kitchell) PROJECT MGR. PHASE/STATUS Design **ARCHITECT PROJECT NUMBER** 9005 Studio-WC PROJECT BUNDLE **CONTRACTOR** TBD Pending Selection PROJECT DELIVERY Lease-Lease Back **INSPECTOR** SITE LOCATION Online Map Link

#### PROJECT SCOPE

Improvements and upgrades to fencing, wayfinding signage and other infrastructure including the installation of the gates at the entrances to resolve safety and security issues. Installation of timed automatic gates to both locations, additional deterrence apparatus, operative arm gate for buses/truck exit. Parking lot conversion into additional parent drop-off/pick-up area.

#### AREAS RECEIVING IMPROVEMENT








#### PROJECT FINANCIALS

PROGRAM FUND 136,000,000 PROJECT COMMITMENTS 168,117 COST TO DATE 16,330
PROJECT BUDGET 1,908,207 COMMITMENT BALANCE 1,740,090 REMAINING BUDGET 1,891,877
BUDGET COMPOSITION MONTHLY/CUMULATIVE COST





#### **PROJECT SCHEDULE**

		Jun-23	Nov-22	Feb-24	Nov-24	Dec-24	Oct-25
Design	Jun-23	Feb-24					
DSA	Feb-24	Aug-24					
Bid/Award	Aug-24	Nov-24					
Construction	Nov-24	Oct-25					
Close-out	Oct-25	Nov-25,					

Bond Program Management Operations Project Report



#### **PROJECT TEAM** PROJECT INFORMATION Paul Cristilli (Kitchell) PROJECT MGR. PHASE/STATUS Design Studio-WC **PROJECT NUMBER** 9301 **ARCHITECT** PROJECT BUNDLE TBD **CONTRACTOR INSPECTOR** Pending Selection PROJECT DELIVERY Lease-Lease Back SITE LOCATION Online Map Link

#### **PROJECT SCOPE**

The overall scope of design work includes monument signage, landscaping, hardscaping, new marquee, and other entrance improvements. The goal is to ensure campus entry is safe and welcoming and respects the architectural style and integrity of the existing buildings.

#### **EXISTING PHOTOS**







41,900

3,347,690

#### PROJECT FINANCIALS

PROGRAM FUND 136,000,000 PROJECT COMMITMENTS 270,472 COST TO DATE PROJECT BUDGET 3,389,591 COMMITMENT BALANCE 3,119,119 REMAINING BUDGET **BUDGET COMPOSITION** 652,331 Construction 346,232 Other Soft Costs 2,391,028 Design

МО	NTHLY/CUMULATIVE COST		
	0.5M	3.8M	
st	0.4M	3.0M	Cost
°C Co	0.3M	2.3M	tive
Montly Cost	0.2M	1.5M	Cumulative Cost
	0.1M	0.8M	Cū
	0.0M	0.0M	
	May-22 Oct-22 Mar-23 Aug-23 Jan-24 Jun-24 Nov-24		
	Preconstruction Cost Construction Cost ••••• Cum	ulative C	ost

#### **PROJECT SCHEDULE**

			Apr-22	Apr-23	Jul-23	Apr-24	Oct-24	Apr-25
Design	4/6/2022	4/6/2023						
DSA	4/7/2023	8/2/2023						
Bid/Award	8/3/2023	11/30/2023						
Construction	12/1/2023	5/1/2025						
Close-out	5/2/2025	5/20/2025						



PROJECT INFORMA	ATION	PROJECT TEAM	Л
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)
PROJECT NUMBER	9302	ARCHITECT	Studio-WC
PROJECT BUNDLE	В	CONTRACTOR	TBD
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection
SITE LOCATION	Online Map Link		

The overall scope of design work includes monument signage, landscaping, hardscaping, new marquee, and other entrance improvements. The goal is to ensure campus entry is safe and welcoming and respects the architectural style and integrity of the existing buildings.

#### AREAS RECEIVING IMPROVEMENT



Apr-22

Apr-23





#### PROJECT FINANCIALS PROGRAM FUND 322,042 COST TO DATE 136,000,000 PROJECT COMMITMENTS 50,841 **REMAINING BUDGET** PROJECT BUDGET 4,121,685 COMMITMENT BALANCE 3,799,643 4,070,844 MONTHLY/CUMULATIVE COST **BUDGET COMPOSITION** 0.6M 4.5M 0.5M 463,013 3.8M **Montly Cost** 0.4M 3.0M Construction 0.3M 2.3M 793,315 Other Soft Costs 0.2M 1.5M 2,907,240 0.1M 0.8M Design 0.0M 0.0M Aug-23 Jan-24 Construction Cost ••••• Cumulative Cost **Preconstruction Cost PROJECT SCHEDULE**

Apr-24

Oct-24

Apr-25

Jul-23



PROJECT INFORM	ATION
PHASE/STATUS	Design
PROJECT NUMBER	9303
PROJECT BUNDLE	В
PROJECT DELIVERY	Lease-Lease Back

Lease-Lease Back
Online Map Link

#### PROJECT TEAM

PROJECT MGR. Paul Cristilli (Kitchell)

ARCHITECT Studio-WC

CONTRACTOR TBD

INSPECTOR Pending Selection

#### PROJECT SCOPE

The overall scope of design work includes monument signage, landscaping, hardscaping, new marquee, and other entrance improvements. The goal is to ensure campus entry is safe and welcoming and respects the architectural style and integrity of the existing buildings.

#### AREAS RECEIVING IMPROVEMENT








#### PROJECT FINANCIALS

SITE LOCATION

PROGRAM FUND 136,000,000 PROJECT COMMITMENTS 171,236 COST TO DATE 48,057
PROJECT BUDGET 1,602,954 COMMITMENT BALANCE 1,431,718 REMAINING BUDGET 1,554,897





#### **PROJECT SCHEDULE**

			Apr-22	Apr-23	Jul-23	Apr-24	Oct-24	Apr-25
Design	4/6/2022	4/6/2023						
DSA	4/7/2023	8/2/2023						
Bid/Award	8/3/2023	11/30/2023						
Construction	12/1/2023	5/1/2025						
Close-out	5/2/2025	5/20/2025						



# PROJECT INFORMATION PHASE/STATUS PROJECT NUMBER PROJECT BUNDLE B PROJECT DELIVERY Lease-Lease Back

# PROJECT TEAM PROJECT MGR. Paul Cristilli (Kitchell) ARCHITECT Studio-WC CONTRACTOR TBD INSPECTOR Pending Selection

#### **PROJECT SCOPE**

The overall scope of design work includes monument signage, landscaping, hardscaping, new marquee, and other entrance improvements. The goal is to ensure campus entry is safe and welcoming and respects the architectural style and integrity of the existing buildings.

#### AREAS RECEIVING IMPROVEMENT

Online Map Link


SITE LOCATION







# PROGRAM FUND 136,000,000 PROJECT COMMITMENTS PROJECT BUDGET 782,071 COMMITMENT BALANCE BUDGET COMPOSITION 86,608 147,796 Construction Other Soft Costs Design

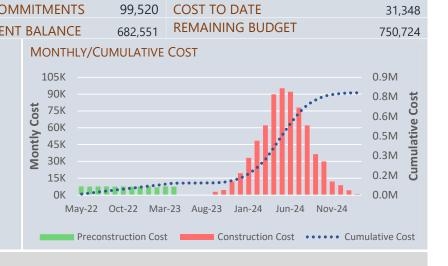

#### **PROJECT SCHEDULE**

PROJECT FINANCIALS

			Apr-22	Apr-23	Jul-23	Apr-24	Oct-24	Apr-25
Design	4/6/2022	4/6/2023						
DSA	4/7/2023	8/2/2023						
Bid/Award	8/3/2023	11/30/2023						
Construction	12/1/2023	5/1/2025						
Close-out	5/2/2025	5/20/2025						



PROJECT INFORMA	ATION	PROJECT TEAM		
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9305	ARCHITECT	Studio-WC	
PROJECT BUNDLE	В	CONTRACTOR	TBD	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	Online Map Link			

The overall scope of design work includes monument signage, landscaping, hardscaping, new marquee, and other entrance improvements. The goal is to ensure campus entry is safe and welcoming and respects the architectural style and integrity of the existing buildings.

#### AREAS RECEIVING IMPROVEMENT







37,325

# PROGRAM FUND 136,000,000 PROJECT COMMITMENTS PROJECT BUDGET 1,659,840 COMMITMENT BALANCE MONTHLY 240K 200K 200K 174,351 Construction Other Soft Costs 1,162,353

Design



163,912 COST TO DATE

#### **PROJECT SCHEDULE**

PROJECT FINANCIALS

			Apr-22	Apr-23	Jul-23	Apr-24	Oct-24	Apr-25
Design	4/6/2022	4/6/2023						
DSA	4/7/2023	8/2/2023						
Bid/Award	8/3/2023	11/30/2023						
Construction	12/1/2023	5/1/2025						
Close-out	5/2/2025	5/20/2025						



## PROJECT INFORMATION PHASE/STATUS PROJECT NUMBER PROJECT BUNDLE B PROJECT DELIVERY Lease-Lease Back

# PROJECT TEAM PROJECT MGR. Paul Cristilli (Kitchell) ARCHITECT Studio-WC CONTRACTOR TBD INSPECTOR TBD

#### **PROJECT SCOPE**

The overall scope of design work includes monument signage, landscaping, hardscaping, new marquee, and other entrance improvements. The goal is to ensure campus entry is safe and welcoming and respects the architectural style and integrity of the existing buildings.

#### AREAS RECEIVING IMPROVEMENT

Online Map Link








#### PROJECT FINANCIALS

SITE LOCATION

PROGRAM FUND 136,000,000 PROJECT COMMITMENTS 407,400 COST TO DATE 55,933
PROJECT BUDGET 5,629,940 COMMITMENT BALANCE 5,222,540 REMAINING BUDGET 5,574,006





#### **PROJECT SCHEDULE**

			Apr-22	Apr-23	Jul-23	Apr-24	Oct-24	Apr-25
Design	4/6/2022	4/6/2023						
DSA	4/7/2023	8/2/2023						
Bid/Award	8/3/2023	11/30/2023						
Construction	12/1/2023	5/1/2025						
Close-out	5/2/2025	5/20/2025						
