





# LOMA ELEMENTARY

## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Improvement in School Grounds, Campus Infrastructure Upgrades, Signage/Marquee Upgrades, Trash Enclosure
PROJECT NUMBER	9304	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	137,064,475	PROJECT COMMITMENTS	1,208,701	COST TO DATE	1,012,840
PROJECT BUDGET	1,251,805	% COMMITTED	97%	REMAINING BUDGET	43,104

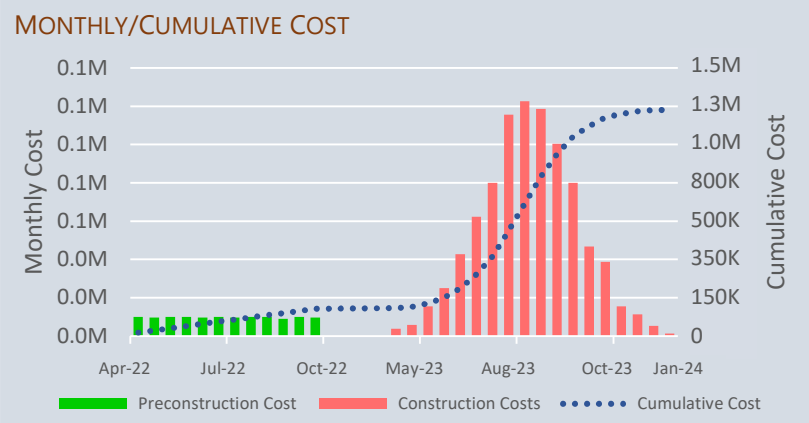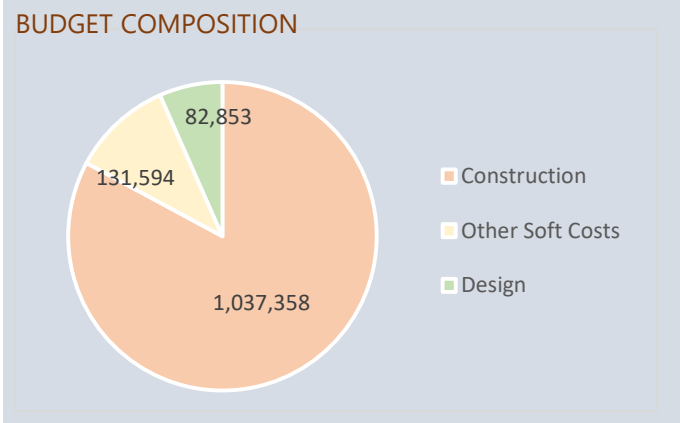

### PROJECT SCHEDULE

Task Name	Duration	Qtr 2, 2022			Qtr 3, 2022			Qtr 4, 2022			Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			
		Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
Design	213 days	[Progress Bar]																											
DSA	23 days																												
Bid/Award	64 days																												
Construction	209 days																												
Close-Out	23 days																												

