



# STEAM ACADEMY

## ENTRY IMPROVEMENTS



PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE Current scope to include pole signage, landscaping, hardscaping, marquee signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.
PHASE/STATUS	DSA	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9408	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	A	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

### ENTRANCE SCHEMATIC



### PROJECT FINANCIALS

PROGRAM FUND	136,235,372	PROJECT COMMITMENTS	115,749	COST TO DATE	26,519
PROJECT BUDGET	719,958	% COMMITMENTED	16.08%	REMAINING BUDGET	604,209

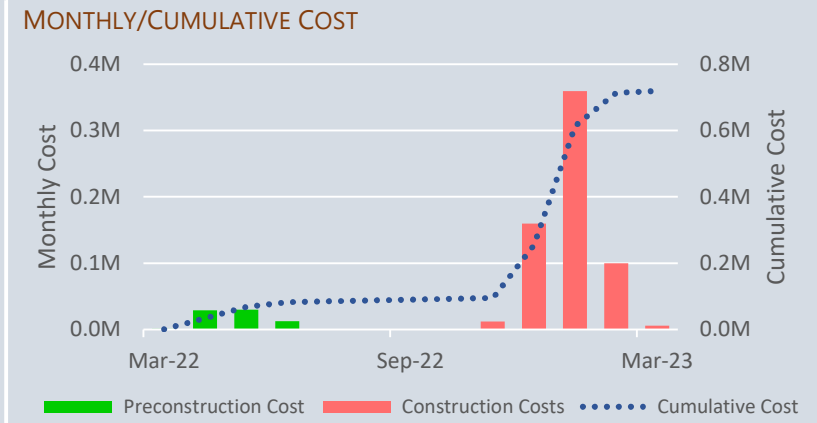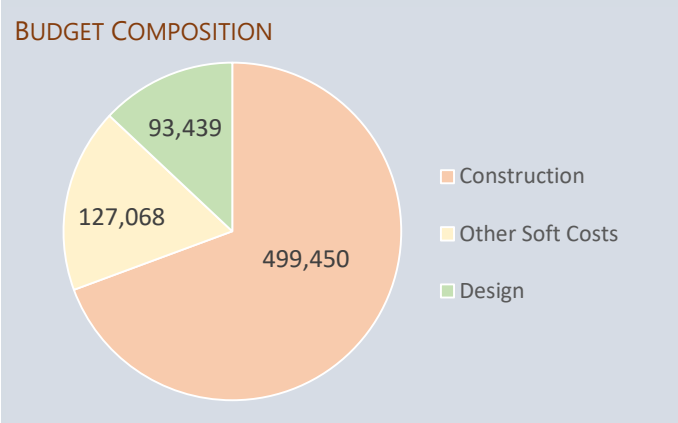

### PROJECT SCHEDULE

	Feb-22	Mar-22	Jul-22	Aug-22	Sep-22	Dec-22	Jan-22	Apr-22
Design	Mar-22	Jul-22						
DSA	Jul-22	Oct-22						
Bid/Award	Jul-22	Nov-22						
Construction	Dec-22	Mar-23						
Close-out	Mar-23	Apr-23						
