



# STEAM ACADEMY

## ENTRY IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	Current scope to include pole signage, landscaping, hardscaping, marquee signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.
PROJECT NUMBER	9408	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	A	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			


### AREAS RECEIVING IMPROVEMENT




### PROJECT FINANCIALS

PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	771,132	COST TO DATE	560,461
PROJECT BUDGET	782,875	% COMMITTED	86%	REMAINING BUDGET	210,670

### BUDGET COMPOSITION

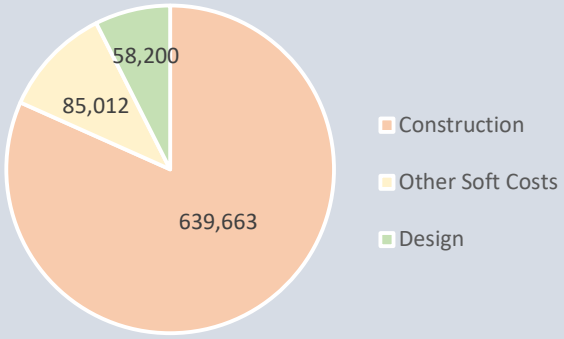

### MONTHLY/CUMULATIVE COST

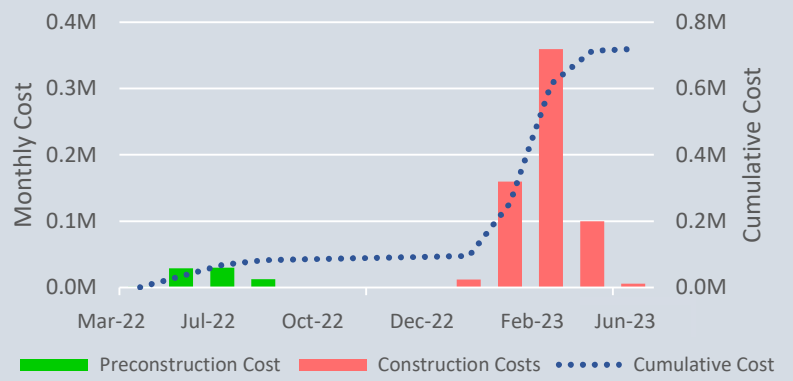

### PROJECT SCHEDULE

