





MARYLAND AVENUE

SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Campus Infrastructure Upgrades & Signage/Marquee Upgrades
PROJECT NUMBER	9105	ARCHITECT	Studio-WC	
PROJECT BUNDLE	C	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	Online Map Link			

PROJECT FINANCIALS					
PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	183,602	COST TO DATE	64,500
PROJECT BUDGET	1,469,319	% COMMITTED	12%	REMAINING BUDGET	119,101

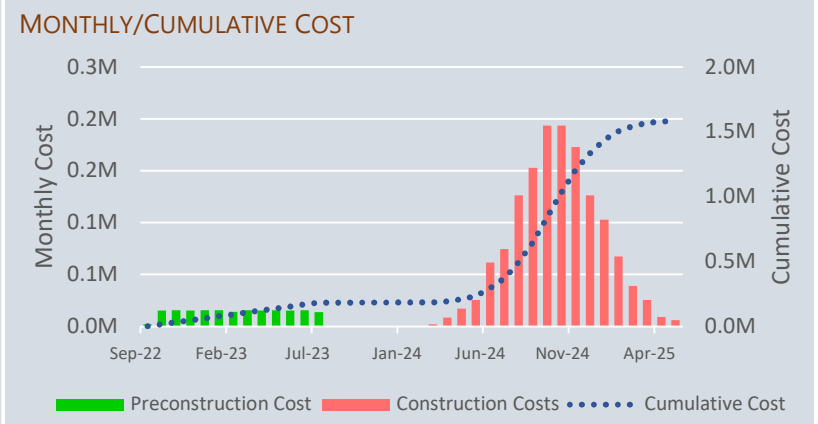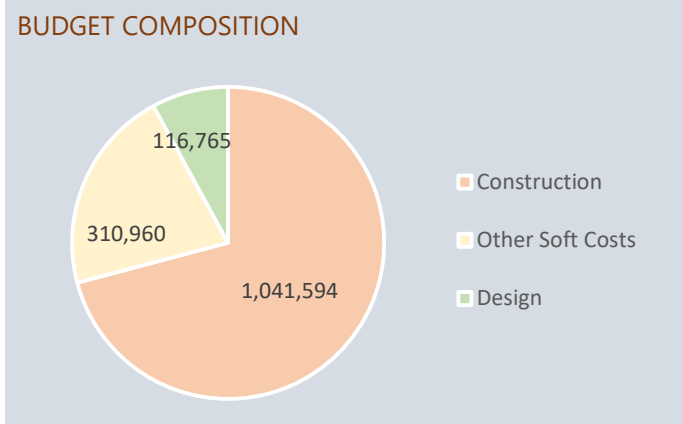

PROJECT SCHEDULE

Task Name	Duration	2022	2023	2024	2025																	
		Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	
Design	245 days																					
DSA	105 days																					
Bid/Award	41 days																					
Construction	261 days																					
Close-Out	22 days																					

