





# STEAM ACADEMY

## ENTRY IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE Current scope to include pole signage, landscaping, hardscaping, marquee signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.
PHASE/STATUS	Closeout	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9408	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	A	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS			
PROGRAM FUND	137,064,475	PROJECT COMMITMENTS	-
PROJECT BUDGET	1,487,265	% COMMITTED	-
		COST TO DATE	1,439,245
		REMAINING BUDGET	-

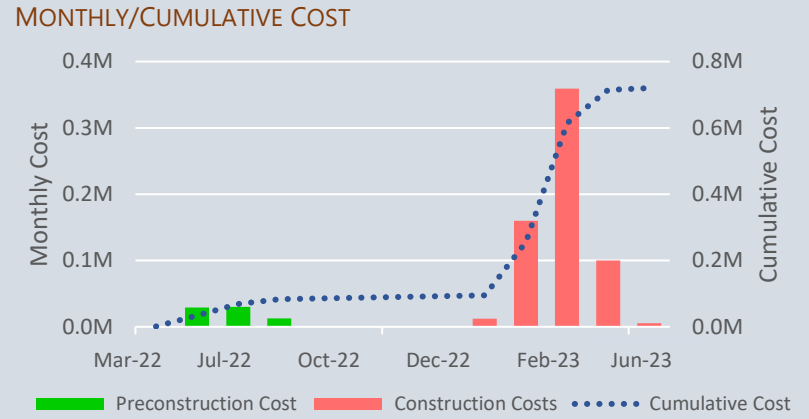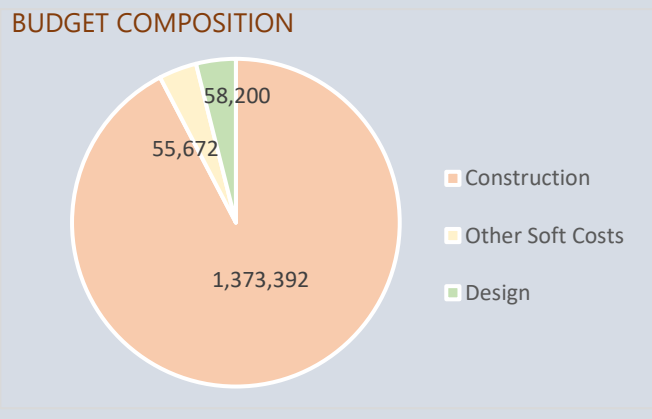

### PROJECT SCHEDULE

Task Name	Jul	Aug	Sep	Oct	Nov	Dec	2023	Jan	Feb	Mar	Apr	May
Design	█											
DSA		█										
Bid/Award			█									
Construction				█								
Close-Out						█						

