



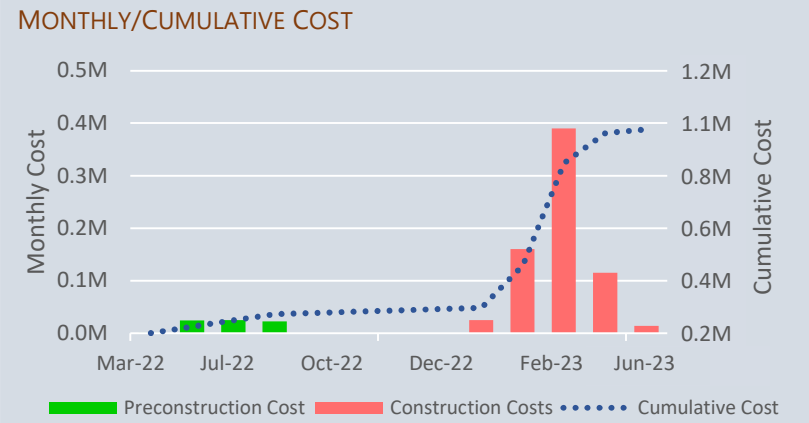

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE Current scope to include monument marquee, landscaping, hardscaping, signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.
PHASE/STATUS	Closeout	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9205	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	A	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS			
PROGRAM FUND	136,424,117	PROJECT COMMITMENTS	-
PROJECT BUDGET	1,011,164	% COMMITTED	-
		COST TO DATE	977,589
		REMAINING BUDGET	-

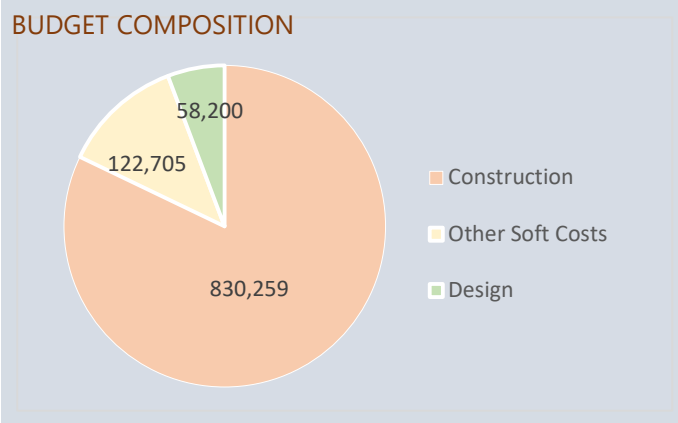

### PROJECT SCHEDULE

Task Name	Jul	Aug	Sep	Oct	Nov	Dec	2023	Jan	Feb	Mar	Apr	May
Design	█											
DSA	█											
Bid/Award			█									
Construction				█								
Close-Out												
