



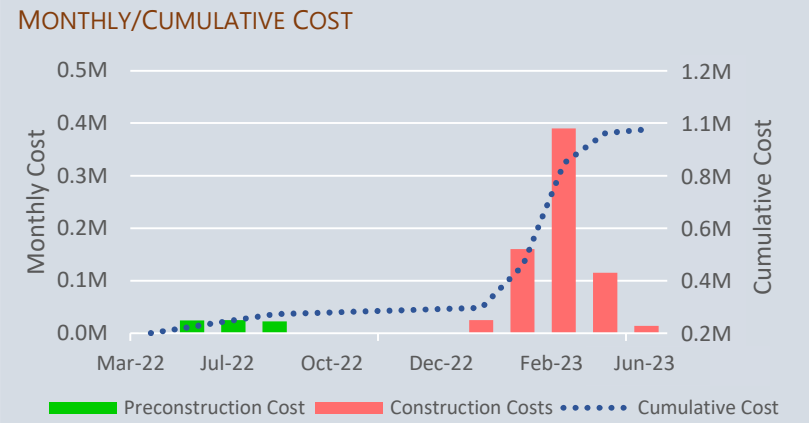

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Closeout	PROJECT MGR.	Paul Cristilli (Kitchell)	Current scope to include monument marquee, landscaping, hardscaping, signage, and/or other general entrance improvements with the goal of ensuring the campus entry is safe and welcoming while honoring the architectural integrity and style of the existing buildings.
PROJECT NUMBER	9205	ARCHITECT	Mosher-Drew	
PROJECT BUNDLE	A	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	1,033,358	COST TO DATE	1,033,358
PROJECT BUDGET	1,080,736	% COMMITTED	96%	REMAINING BUDGET	47,378

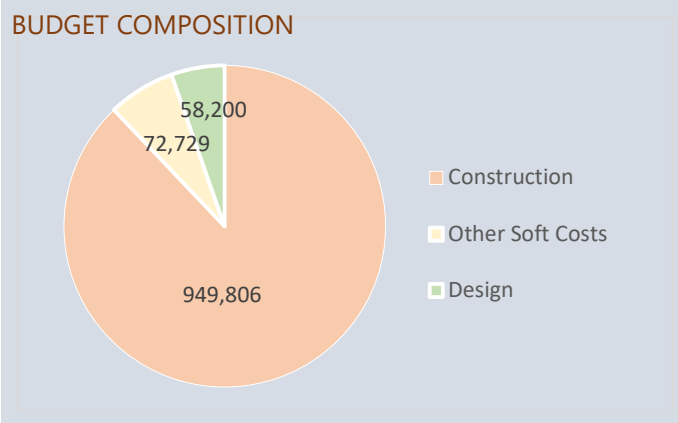

### PROJECT SCHEDULE

Task Name	Jul	Aug	Sep	Oct	Nov	Dec	2023	Jan	Feb	Mar	Apr	May
Design	█											
DSA	█											
Bid/Award			█									
Construction				█								
Close-Out												
